

Strategic Exit Evaluation Report

Strengthening the Right to Education for Child Laborers in Dhaka City

Date: 2025.12.15

Prepared by

Moon Suk HONG, Ph.D.

Yoon Joo JIN, Ms. Ph.D. Candidate

Research Institute of Migration and Multiculturalism
International Development and Cooperation Major
School of Social Science, Busan University of Foreign Studies

List of Contents

Executive Summary-----	3
I. Introduction-----	4
II. Objectives and Scope of the Evaluation -----	5
III. Evaluation Methodology-----	9
IV. Key Findings-----	16
Relevance, Coherence and Context-----	16
Efficiency -----	17
Effectiveness -----	24
Impact (Readiness) and Sustainability -----	28
Analysis of Enablers and Constraining Factors -----	31
V. Conclusion and Recommendations-----	34
Appendices-----	34

Abbreviations

AP	Area Program
BBS	Bangladesh Bureau of Statistics
BED	Basic Education Diploma
BUFS	Busan University of Foreign Studies
CDP	Community Development Program
CRD	Centre for Research and Development (Bangladesh)
CLCLMC	Community Led Child Labour Monitoring Committee
CLEP	Child Labour Elimination Platform
DAC	Development Assistance Committee
DQA	Data Quality Assurance
DRR	Disaster Risk Reduction
ESDO	Eco-Social Development Organization (Bangladesh)
FGD	Focus Group Discussion
IDI	In-Depth Interview
ILO	International Labour Organization
KII	Key Informant Interview
KOICA	Korea International Cooperation Agency
M&E	Monitoring and Evaluation
MoE	Ministry of Education
MoLE	Ministry of Labour and Employment
MoPME	Ministry of Primary and Mass Education
MOWCA	Ministry of Women and Children Affairs
NCLS	National Child Labour Survey
NFE	Non-Formal Education
NGO	Non-Governmental Organization
OECD	Organization for Economic Co-operation and Development

Executive Summary

This report presents the findings of the *Strategic Exit Evaluation* conducted for the “Strengthening Right to Education for Child Laborers in Dhaka City” project, jointly implemented by ChorogUsan for children in partnership with Educo, as well as Eco-Social Development Organization (ESDO) in Bangladesh. The Korea International Cooperation Agency (KOICA) from the people of the Republic of Korea, funds the project. It aims to improve access to education and protect the rights of children engaged in hazardous labor in Dhaka’s slum areas, addressing both educational and social vulnerabilities to ensure that children can continue their learning and holistic development safely. Views from students, parents, and duty bearers, the below highlighted significant progress in education access and awareness, while also revealing persisting challenges.

- Student enrollment and aspirations, evaluation findings show that 86.3% of students expressed a strong willingness to continue to lower secondary school, with 97.1% of girls and 75.6% of boys willing largely. Qualitative insights from FGDs revealed that students are motivated and enjoy attending bridge schools, appreciating interactive learning methods and teacher support. Parents acknowledged their children’s improved learning and motivation but noted practical barriers such as financial hardship, household responsibilities, and safety concerns, which may reduce actual transition rates. Second, regarding learning outcomes, all 271 surveyed students expressed their intention to complete it by the end of 2025.
- In efficiency and effectiveness of project delivery, it achieved 100% enrollment (800 children) and fully achieved the targets for school materials and meals, reaching 1,190 boys and 1,210 girls (target: 1,200 each). To date, 2,211 bridge school students have participated in the awareness sessions, which is slightly below the target of 2,400; however, participation is expected to increase. On the contrary, parent participation was strong, although male participation fell significantly below the target of 1,200, with 858 males and 1,745 females attending. FGD discussions indicated that parents found the sessions informative and motivating, particularly regarding the importance of continuing education for girls.
- The project exceeded targets in learning support interventions: psychosocial counseling reached 973 boys and 1023 girls (target: 120 each), and extra coaching reached 1094 boys and 1087 girls (target: 600 each). FGDs confirmed that students, especially girls, found counseling sessions and extra coaching helpful in improving confidence, motivation, and academic performance. In addition, student awareness improved to 40.6% from a baseline of 14.98%, meeting the target of 40%. Among duty bearers, awareness rose from 20.26% to 60.8%, exceeding the target.

Building on the clear achievements of Project Phase 1, the evaluation team proposed the following additional considerations for the expansion of project and the possible development for program level contribution in the future.

- First, the policy and institutional contributions related to the right to education and child labor, which were included as outputs of Phase 1, need to be emphasized. The team proposes emphasizing policy and institutional improvements, such as expanding the role of the Child Labor Eradication Platform (CLEP) to enhance the right to education and strengthening the role of the Community-Led Child Labor Monitoring Committee (CLCLMC), and including these in the project model.

- Considering the current compulsory education age under Bangladeshi law, we propose that ChorogUsan for children and Educo contribute to improving policies and systems to expand the age of primary education and the scope of education provision. In particular, for this first project, ChorogUsan for children needs to expand its achievements by securing a civil society space that can contribute to system improvement through collaboration with the Child Labor Eradication Platform (CLEP), which Educo leads and collaborates with 21 organizations, including Save the Children, Educo, BSA, ActionAid, SOS, and Good Neighbors.
- Third, we propose developing the Bridge School model, a specialized education program designed to address child labor issues, a key initiative of the ChorogUsan for children, and implementing it in several Asian and African countries. If expanded into a strategic civil society partnership, we recommend actively considering linking it with national systems, including the establishment of a national digital platform for child protection and expansion of the right to education in Bangladesh, secondary-level vocational training, and skills and digital literacy.

I. Introduction

ChorogUsan for children, in cooperation with Educo in Bangladesh, has been carrying out the "Child Protection Project in Dhaka, Bangladesh" from August 2018 to December 2021 with its own funds to promote basic education rights for child laborers in the Dhaka region of Bangladesh. Since then, it has been selected as the Korea International Cooperation Agency (KOICA)'s Civil Society Cooperation Project and has been carrying out the project to promote basic education rights for children working in slum areas of Dhaka, Bangladesh, since December 2022.

As this year is the final year of the first phase of the project, it plans to conduct an end-of-phase evaluation. Through this evaluation, we aim to measure and analyze the performance of the project, and, based on the analysis results, derive lessons and implications that can be applied when planning or promoting future follow-up projects. This evaluation project is primarily aimed at analyzing the progress of projects that KOICA-ChorogUsan for children's 2022-2025 <Strengthening Right to Education for Child Laborer in Dhaka City> has conducted and to provide implications for future project implementation by examining working factors and challenges in the process of achieving these outcomes.

In Bangladesh, child labour remains one of the most pressing social challenges, particularly in urban centers such as Dhaka, where thousands of children are engaged in hazardous and exploitative work. According to the reports of the National Child Labour Survey 2022, over 1.2 million children in Bangladesh were involved in labour, with a significant concentration in informal urban sectors such as transport, domestic service, garments, recycling, and small-scale workshops. Recently, the number of working children has increased to approximately 3.54 million; of these, 1.07 million are involved in hazardous work. Children in urban areas, including those in Dhaka, constitute a significant share of this number (BBS, 2024, Centre for Research and Development, 2025). Working children are often subjected to long hours, unsafe working conditions, and limited access to basic services such as healthcare and nutrition, which significantly impacts their physical, cognitive, and social development (ILO, 2023; Save the Children, 2022, CRD, 2025). Moreover, social stigma, first-generation learning challenges, and inflexible school schedules further limit opportunities for working children to continue formal education (BBS, 2022, re-cited in the CRD, 2025).

Over the past decades, it has been reported that Bangladesh has made significant progress in addressing child labor and promoting inclusive education, yet challenges remain, particularly in urban areas such as Dhaka. At the policy level, the Government of Bangladesh has been demonstrating a commitment to eliminating child labor and promoting inclusive education in recent years (CRD, 2025). Key policy frameworks include the National Child Labor Elimination Policy (2010), the National Education Policy (2010), and the 8th Five-Year Plan (2021–2025), all of which emphasize education as a fundamental tool for eradicating child labour and achieving equitable growth. Globally, the project aligns with the Sustainable Development Goals (SDGs)—particularly SDG 4 (Quality Education), SDG 8.7 (End Child Labor in All Its Forms), and SDG 10 (Reduced Inequalities)—and contributes to the broader Education for All (EFA) and UN Convention on the Rights of the Child (CRC) commitments (UN, 2015; UNESCO, 2015, Hong 2024).

Within this context, the “Strengthening the Right to Education for Child Laborers in Dhaka City” project seeks to bridge the gap between policy intent and realities by creating accessible, flexible, and

inclusive education opportunities for child laborers in Bangladesh. The project team has emphasized that it is essential to consider the socio-economic realities that perpetuate child labor and hinder access to education in Dhaka City, in order to understand the project's significance in Bangladesh. As the economic hub of Bangladesh, Dhaka city attracts a large influx of low-income migrant families from rural areas. Many of these families depend on the income generated by their children, leading to high rates of child labor in the informal sectors. Working children in Bangladesh have often faced multiple deprivations: long working hours, exposure to hazardous conditions, and lack of access to schooling, poor nutrition, and psychosocial stress (CRD, 2025).

Findings from past assessments such as National Child Labour Survey (2022), UNICEF (2023) and CRD (2025) have commonly explained that many working children are first-generation learners, facing limited parental awareness about the value of education and institutional barriers such as inflexible school schedules, inadequate learning support, and social stigma. Statistical evidence from the Dhaka division shows a clearer picture of child labor.

This division alone accounts for approximately 340,000 child laborers aged 5-17, making it the second-highest number of such children (BBS, National Child Labour Survey 2024, re-cited from the CRD, 2025). In the major slum settlements of Dhaka, about 15% of children aged 6-14 are reported to be both out of school and engaged in full-time work, while by age 14, almost half are working (Quattri, M. & Watkins, K., 2016, re-cited in CRD 2025). These complex socio-economic challenges necessitate an integrated, rights-based approach that combines education, protection, and community sensitization to sustainably reduce child labour.


In response to these challenges, the “Strengthening the Right to Education for Child Laborers in Dhaka City” project was launched as a three-year initiative implemented by Educo Bangladesh in partnership with the Eco-Social Development Organization (ESDO), with financial support from KOICA and ChorogUsan for children. The project aims to uphold and promote the right to education for children engaged in or at risk of child labor within selected areas of Dhaka city. The project targets approximately 800 working and out-of-school children in selected urban areas of Dhaka, aiming to ensure their right to education while reducing engagement in hazardous labor. Key activities include establishing Bridge Schools with flexible schedules, providing learning materials and psychosocial support, conducting community awareness campaigns, and building the capacity of teachers, caregivers, and local education authorities. The project also sought to strengthen linkages between non-formal and formal education systems to ensure sustainable reintegration of children into mainstream schooling, contributing to global educational development goals such as SDG 4 (Quality Education) and SDG 8.7 (Ending Child Labor).

II. Objectives and Scope of the Evaluation

The core objective of the evaluation focused on four evaluation criteria - efficiency, effectiveness/impact, sustainability, coherence, and cross-cutting issues, derived from the six evaluation criteria of the OECD DAC (relevance, coherence, efficiency, effectiveness, impact, and sustainability), as well as the evaluation guidelines for international development cooperation. In recent years, approaches and tools such as Theory-Based Evaluation (TBE) and Theory of Change (ToC) have been actively employed in the planning, monitoring, and evaluation of ODA projects, going beyond the conventional use of the Project Design Matrix (PDM) (Hong et al., 2019). In particular, for projects in the field of education, there has been growing criticism that the traditional evaluation methodology focused on input-output logic models and quantitative indicators has limitations in capturing the complexity of educational interventions. As a result, there is increasing interest in and use of qualitative evaluation methods using the Theory of Change.

The core evaluation questions are finalized, based on the communications between the evaluation team and CFK. The scope of the exit evaluation is decided based on realistic decisions based on the communication between the CFK and evaluation team, given the time and resources available for implementing the evaluation. From this perspective, the project-level ToC was first developed based on the existing Project Design Matrix (PDM). The Figures below present the As-is Model of the project, as well as the To-be Model of the project. The suggested theory model has been further expanded and it will be explained in the section for impact and sustainability (see the details in the V. Analysis of Enablers and Constraining Factors).

Figure 1. Theory of Change-As-is Model

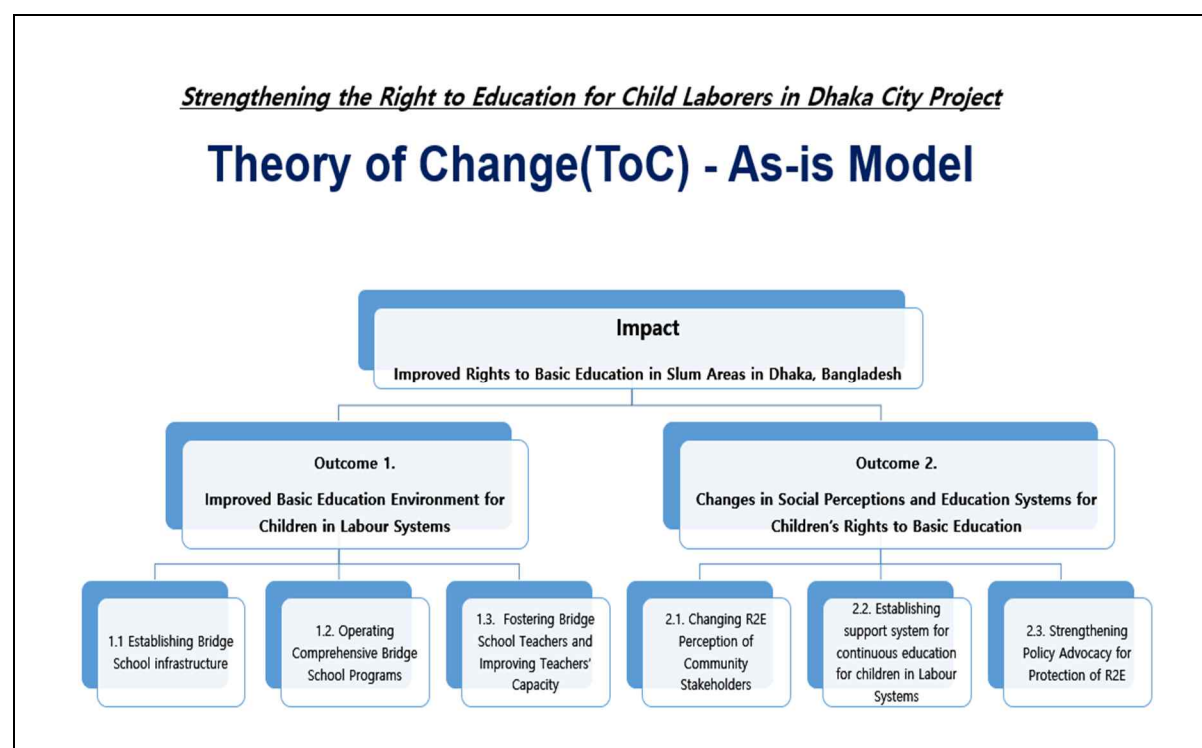

* Developed based on existing Project PDM (2025)

This review will evaluate both the achievement of specific PDM performance targets and capture broader outcomes (intended and unintended) that emerged during implementation. It will also identify key change mechanisms, including the working factors and challenges. The core M&E questions and matrix of the projects, and they are; (i) efficiency, (ii) effectiveness and impact(preparedness), as well as (iii) sustainability. The details of the evaluation matrix are listed below. The below include =s some of the core question areas – *Efficiency, Effectiveness and Impact (Preparedness) and Sustainability* was reviewed in details:

Efficiency

- (Output-Input Efficiency) Was the project efficiently implemented by leveraging the expertise of domestic and local partner organizations? (i.e., completion of the BED of child laborers as outputs of this project)
- (Cost efficiency) Was the project completed within the planned budget?
- (Time efficiency) Was the project implemented according to the planned schedule? (ie. Accelerated learning curriculum, and accelerated teaching and learning)

Effectiveness

- (Achievement of outputs and outcomes) Were the outputs and outcomes proposed in the PDM achieved?
- (The extent to which the project ensured inclusiveness and equity for vulnerable populations) Were the project beneficiaries fairly chosen among beneficiaries from diverse backgrounds of children? Were the project's outcomes and benefits fairly distributed among beneficiaries from diverse backgrounds of children (i.e. sex, family background, parents' education level)?
- (Socio-economic/institutional impact of the project) Did the project contribute to the improvement and expansion of policies or systems related to BED/NFE or CLEP/CLCMC in the partner country (readiness)?

Impact (Preparedness)

- (Achievement of outcomes and goals) Were the outcomes and goals proposed in the PDM and TOC achieved?

Sustainability

- (Financial and institutional capacity) Does the partner country have the financial capacity (budget) to continue the project's outcomes after its completion? Are there institutional measures (laws, policies, and systems) in place to support continuation of the project's results?
- (Systems for the management of human resources) Are dedicated personnel in place to ensure the continuity of the project after its completion? Has the project contributed to building an environment where the professional capacity can be sustained and scaled up even after the project's completion?
- (Systems for the professional, community, policy, knowledge network) Has a professional, community or/and policy/knowledge network been established and maintained that can be sustained and expanded even after the completion of the project?

Table 1. Evaluation Matrix

Standard	Criteria	Key Questions
Efficiency	Cost efficiency Output-to-input efficiency	- Was the project completed within the planned budget? - Time efficiency - Was the project implemented according to the planned schedule? - Was the project efficiently implemented by leveraging the expertise of domestic and local partner organizations? (i.e., completion of BED of child laborers as outputs of this project)
Effectiveness- Impact (Preparedness)	Achievement of outcomes, outputs and goals Socio-economic/institutional impact of the project	- Were the outputs, outcomes, and goals proposed in the PDM achieved? - Were the project beneficiaries fairly chosen among beneficiaries from diverse backgrounds of children? - Were the project's outcomes and benefits fairly distributed among beneficiaries from diverse backgrounds of children (sex, family background, parents' education level)? - Did the project contribute to the improvement and expansion of policies or systems related to BED/NFE or CLEP/CLCMC in the partner country (readiness)?
Sustainability	Financial and institutional capacity Systems for the management of human resources	- Does the partner country have the financial capacity (budget) to continue the project's outcomes after its completion? - Are there institutional measures (laws, policies, and systems) in place to support continuation of the project's results? - Are dedicated personnel in place to ensure the continuity of the project after its completion? - Has the project contributed to building the environment where the professional capacity can be sustained and scaled up even after the project's completion? - Has a network been established and maintained that can be sustained and expanded even after the completion of the project?
	Factors regarding sustainability Factors regarding sustainability	- What are the structural factors within the partner country and its institutions that facilitate sustainability? (Working factors) - What are the structural factors within the partner country and its institutions that hinder sustainability? (Challenges)

III. Evaluation Methodology

3.1. Introduction of Evaluation Methods

A mixed methods approach, applied in the strategic evaluation, was needed to provide a more complete understanding of complex issues by combining the strengths of both quantitative and qualitative approaches. The combination of various methods can enhance the validity of findings, capture diverse perspectives, and support more informed decision-making. This evaluation has employed a mixed-method approach, beginning with a comprehensive desk review to guide the evaluation design, inform the development of data collection tools, and support validation of the findings. Both the Korean evaluation team and the end-line assessment team, in order to generate measurable evidence, and to identify statistical trends across key indicators, gathered quantitative data. Together, these mixed methods enabled a robust analysis through triangulation, ensuring both accuracy and depth in interpreting the study's outcomes.

Gathering information on the evaluation target was based on a literature review and interviews with domestic and international stakeholders, and a preliminary plan for conducting a field survey. Conducting a field survey in Bangladesh. Reviewing the project site and project performance. Reviewing achievements by performance indicator: Based on the results of a survey conducted by a local consultant, reviewing the achievements of each outcome and output, and conducting a preliminary analysis of project performance.

Table 2. Introduction of Methodology

Phase	Steps	Key Methods
Phase 1	Evaluation Planning and Design	Desk Review Online Interviews Development of Theory of Change (ToC) Project-level Systematic Output-outcome Harvesting (OH)
Phase 2	Domestic and International Research Period	Online Interviews Questionnaires Field Interview Questionnaires Survey Inception & Technical Assistance Methods Triangulation
Phase 3	Field Survey Results Sharing and Follow-up Workshop	Field Evaluation Field Survey Results Sharing Workshop Contents Triangulation (Part 1)
Phase 4	Analysis of Evaluation Results	Contribution Analysis(CA) Contents Triangulation (Part 2) Write-up the Report

3.2. Detailed Evaluation Methods and Tools

Phase 1: Evaluation Planning and Design

Evaluation planning involves literature review (domestic and international literature and project data), evaluation matrix development, and evaluation tool development.

Phase 2-3: Domestic and International Research Phase

All items are all assessed through questionnaires, interviews, and literature reviews. Efficiency: Evaluation rating scale, questionnaire (5-point scale), in-depth interviews (II, FGI), project-level systematic outcome reporting (OH), and success story methodology (SCM).

- Efficiency: questionnaire (5-point scale), in-depth interviews (II, FGI), questionnaire (5-point)
- Effectiveness and Impact (Readiness): questionnaire (5-point scale), project-level Systematic Output-outcome Harvesting (OH), in-depth interviews (II, FGI), questionnaire (5-point scale)
- Sustainability (Readiness): Rating scale, questionnaire (5-point scale), Time of Change Model (ToC) analysis or Success Case Study Method (SCM)

There are various quantitative evaluation methods applied for this evaluation between September and November 2025, including the CRD's end-line assessment and they are as below:

- Quantitative Methodology: Data collection methods and tools: In terms of quantitative data collection, Household surveys were conducted using a structured survey questionnaire that helps to minimize interviewer bias and ensure that data are collected in a consistent and standardized manner.
- Detailed Plan for the Pilot Testing: The pilot testing began on 13 October, following the incorporation of feedback from Educo Bangladesh and ChorogUsan for children on the draft data collection tools. A four-member team, led by the Field Research Manager, conducted the pilot across four bridge schools -3 (Rayerbazar), 4 (Jafrabad), 5 (Bowbazar), and 6 (Balur Math).
- A total of eight (08) surveys for the end-lien assessment were conducted, with two surveys per school- one with parents and one with students to capture both perspectives. Additionally, one Focus Group Discussion (FGD) was conducted with students at BS 4, one In-Depth Interview (IDI) with parents at BS 4, and one Key Informant Interview (KII) with a teacher at BS 6 to assess the clarity, flow, and relevance of the qualitative tools. The insights gained from the pilot were utilized to refine and finalize the survey instruments and field procedures before commencing the main data collection.
- Sampling design for quantitative survey: A stratified random sampling technique was applied to capture diverse perspectives across different stakeholder groups, bridge school locations, sexes, and respondent types (students and parents). From each stratum, respondents were randomly selected to minimize selection bias and ensure representation across all project sites. This approach balanced inclusivity with statistical rigor, making the data suitable for comparative analysis across groups and project areas.

However, during the end-line assessment, the field assessment teams from CRD has pointed out that the findings may not be fully generalizable to all child labourers in Dhaka or other regions. Despite this limitation, the results of the end line assessment provided robust and reliable evidence on project-level outcomes and valuable lessons for similar urban child labour interventions. According to end-line assessment, Cochran's formula for a known population was used to determine a representative sample from each bridge school community, following standard practice. The sample size was calculated using

a 95% confidence level, a 0.05 margin of error (5%), and an estimated proportion of 50%. The formula used is as follows:

Table 3: Sample Size Calculation

$n = \frac{z^2 p \cdot q \cdot N}{z^2 \cdot p \cdot q + (N - 1)e^2}$ $n = \frac{1.96^2 * 0.5 * 0.5 * 800}{1.96^2 * 0.5 * 0.5 + (800 - 1) * 0.05^2}$ $n = \frac{768.32}{2.9579} = 260$	In the Sample Estimate, the given value is: N = 800 (Total students of bridge school) e = 0.05 (Standard Practice 5%) significance level or admission error margin p = 0.5 (we considered that the proposition of defectiveness or success for the indicator is equal q = factor q (1 - .5) = 0.5 z = 1.96 (value of a standard normal variable 95% confidence level)
---	--

According to the CRD's end-line assessments, the estimated total sample size for children was 260, and an equal sample size was determined for parents, resulting in a total estimated sample of 520 respondents. To account for potential non-responses or data collection errors, a 5% Non-Response Rate (NRR) was added. The adjusted sample size was therefore calculated as follows: Sample size with NRR = $(520 \times 0.05) + 520 = 546$ (approximately)

As for the Korean evaluation team and the end-line assessment teams, conducting qualitative method based evaluation activities were as important as quantitative method based activities. Qualitative methodology: The study employed in-depth interviews (IDIs), focus group discussions (FGDs), key informant interviews (KIIs), field observations, and case studies, using standardized guides and checklists to ensure reliability and validity. Qualitative data were collected from students, parents, teachers, employers, community members, government stakeholders, and project and partner staff to capture diverse perspectives and contextual insights.

- Theory of Change Analysis (TOCA): In this evaluation, qualitative theory of change analysis was conducted in order to identify the project model's design, impact-outcome level result chain review, as well as analysis of enablers and constraining factors
- Contribution Analysis (CA): In this evaluation, qualitative analysis called contribution analysis (CA) was conducted in order to assess the contribution of project activities and outputs for creating impact, rather than measuring attribution.
- Focus Group Discussions (FGDs)¹: In this evaluation, 12 FGDs in total were conducted. Korean team during the field study conducted 4 FGDs and the end-line assessment team conducted 8 FGDs. These include 8 bridge school communities, with participants including students, parents, teachers, and community members. Each FGD involved 8–12 participants, and intersectional categories such as sex, age, education, and occupation were considered to ensure diverse perspectives. Guiding questions and a checklist were used to facilitate

¹ Focus group discussions (FGDs) are a qualitative method that gathers insights from a small group of participants, typically 8 to 12 people with similar backgrounds. Guided by a moderator, participants engage in an open and structured discussion on specific topics of interest. FGDs are useful for exploring shared experiences, opinions, and attitudes, with the moderator ensuring all key issues are covered while encouraging natural interaction among participants.

discussions, with an open-ended and exploratory approach employed by a qualitative researcher to encourage rich insights. Korean team has more focused on examining possible outcomes and future implications that are involved with the under-examined achievements to do with activities of CLEP and CLCLMC.

- Key Informant Interviews (KIIs)²: In this evaluation, 20 KIIs in total were conducted. Korean team during the field study conducted 8 KIIs and the end-line assessment team conducted 14 KIIs. These KIIs included representatives from the Ministry of Labour and Employment, Ministry of Education, project staff (Educo), partner staff (ESDO), bridge schoolteachers, employers, the Secretary of the Counsellor Office, members of CLEP, members of CLCLMC, and Education Officers from the City Corporation Education Department.

Step 4: Analysis of Evaluation Results³

The analysis of evaluation results was based on the "International Development Cooperation Evaluation Manual" published by the Office for Government Policy Coordination (2023). Evaluation levels were assigned for each of the five evaluation criteria: adequacy, efficiency, effectiveness/impact, sustainability, and consistency. However, scoring system was not applied for this evaluation to calculate the evaluation grading. In the categories for impact (readiness), sustainability and analysis for recommendations, mainly qualitative analysis, including ToC analysis and contribution analysis were conducted in order to develop detailed suggestions for the Korean stakeholders including KOICA. These mixed methods approach for analysis enabled an organized and flexible presentation of various findings. For cross-cutting issues, since the content is not included in each evaluation criterion, separate scoring was not provided and was described as a separate item.

- Data analysis: The qualitative data collected through FGDs, IDIs, and KIIs were analyzed using a thematic analysis approach. Themes and patterns were identified across participant groups by extracting relevant content and comparing findings across data collection methods, challenges, and contextual factors pertinent to the study
- After the team's data collection, the dataset was cleaned and prepared for analysis. Including CRD's end-line assessments, there are various quantitative data were entered into Excel and analyzed using pivot tables to generate frequencies, percentages, averages, and cross-tabulations across different bridge schools, genders, and respondent groups (students and parents).
- Respondent-wise data collection plan: The table below presents the respondent categories, data collection methods, sample sizes, and tools used in this study to ensure comprehensive and reliable collection of both qualitative and quantitative data
- Field survey results sharing and follow-up workshop: the workshop was organized in Bangladesh. Sharing field survey results seminar will be organized as the follow-up activity in Seoul to discuss the follow-up project strategies

² Key informant interviews (KIIs) are conducted with individuals who possess specialized knowledge or experience on a particular topic or community. Informants are purposefully selected for their expertise and ability to provide valuable insights. Using flexible interview guides, KIIs follow an informal, conversational style that allows the interviewer to probe deeply and explore issues in detail, capturing nuanced perspectives relevant to the study's objectives.

³ While the detailed scoring system and grading criteria for each evaluation criterion will be reviewed by the donor agency in the future, this strategic evaluation team did not rate based on the KOICA evaluation rating system.

- Discussing Follow-up Actions: To assess the effectiveness, impact, and sustainability of the project, this evaluation will include policy and systemic discussions that project implementers were unable to independently assess during the original project period.

3.3.Exit Evaluation Implementation Strategy and Quality Assurance

The below tables introduce the members of evaluation teams and their roles and responsibilities, reporting and review mechanism, as well as process of quality assurance of this evaluation project.

Table 4. Evaluation Team:

Position	Names	Roles and Responsibilities
Strategic Exit Evaluation (Korea and Bangladesh)		
Principal Investigator (PI)	Moon Suk HONG, Ph.D. • Director, Research Institute of Migration and Multiculturalism • Professor, Chair, International Development and Cooperation Major • Busan University of Foreign Studies	In charge of the evaluation project Writing up the report in English Evaluating outcome1, 3 (policy-system changes, education-related outcomes-outputs)
Evaluation Assistance	Yoon Joo JIN, Ms. Ph.D. Candidate • Researcher, Research Institute of Migration and Multiculturalism • Busan University of Foreign Studies	Communication and logistics Writing up the report in Korean Evaluating outcome2 and related outputs (labour relations)
End-line Assessment (Bangladesh)		
Collaborating Team	Centre for Research and Development (CRD) in Bangladesh	Conduct end-line assessment (focused on key indicators and quantitative surveys)

Table 5. Reporting and Reviewing Mechanism.

Phase	Information Sharing	Collections of Comments
Phase 1	Evaluation Plan	ChorogUsan for children Team
Phase 2	Online Interviews Questionnaires Field Interview Questionnaires (Draft) (EduCo) Survey Inception (3-4 Items in the Existing Questionnaire) + TA	ChorogUsan for children Team EduCo Team
Phase 3	Field Evaluation Capacity Building Workshop Success Case Method Interview	ChorogUsan for children Team EduCo Team
Phase 4	Writing-up the Report	ChorogUsan for children Team

Table 6. *Quality Assurance*

Phase	Implementation Team	External Specialists
Phase 1 Evaluation Plan	ChorogUsan for children Team	
Phase 2 Documentation Analysis and Online Interviews	ChorogUsan for children Team EduCo Team	Three Experts Validation (Education, Labour Relations, Southeast Asia Specialist)
Phase 3 Field Evaluation	ChorogUsan for children Team EduCo Team	Three Experts Validation (in Bangladesh) (Education, Child Labour, Youth Labour)
	ChorogUsan for children Team EduCo Team	Cross-team Review for CRD Data between two country third party teams
Phase 4 Writing-up the Report	ChorogUsan for children Team	Three Experts Validation (Education, Labour Relations, Southeast Asia Specialist)

3.4. Limitations and Ethical Considerations

The evaluation team's evaluators have read and signed the Code of Ethics for Children as third-party specialists in order to engage with Child Fund partners as well as children in the project sites. The team has complied with all detailed provisions of this Code of Ethics throughout the entire evaluation process. To ensure the objectivity, fairness, and reliability of evaluations, which are core principles of evaluation ethics of OECD DAC as well as KOICA Evaluation Guidelines, and to minimize any negative impact on the subjects of evaluation, the team will adhere to these principles throughout the entire evaluation process.

Although approved methodology is strictly applied, the study team considers limitations of the study in several issues. For instance, the end-line assessment team reported that during data collection, the assessment team faced several challenges that required adaptive strategies to ensure data quality and inclusivity. Key challenges are addressed and outlined below:

- **Difficulty in Reaching Fathers:** Fathers were often unavailable during school hours due to work commitments or, in some cases, not living with their children because of multiple marriages. Enumerators conducted visits during evening hours or at workplaces, and when necessary, replaced unavailable respondents with appropriate alternatives while maintaining gender balance.
- **Low Willingness among Parents:** Some parents were initially reluctant to participate or remain for the full duration of interviews. The team explained the purpose and importance of the study for future project implementation, which helped improve cooperation and engagement.
- **Locational Difficulties:** It was initially challenging to locate the Bridge Schools due to the absence of banners or visible identifiers. With guidance from local residents, the exact locations were identified and assessed.
- **Age Gap among Students:** The students were of mixed ages, which created difficulties during FGDs. Senior students tended to dominate, while younger ones responded non-verbally. Enumerators facilitated discussions carefully to encourage equal participation from all age

groups.

- Korean experts led the contribution analysis: Due to time constraints, six Korean specialists conducted the contribution in November and December. If the feedback from the Educo dose not correspond with the outcomes of CA, the Korean team intends to conduct the further collect contribution survey results from the Bangladesh stakeholders after the completion of the project.

In the case of the Korean experts' field evaluation, the evaluation period in Dhaka was limited; thus, the CRD assessment team members mainly conducted field observations. As field observation is a qualitative method used to systematically record behaviors and interactions in their natural settings. In this evaluation, CDR's observation noted helped researchers understand real-life contexts, validate data from other sources, and capture non-verbal cues or environmental factors. In this study, field observation was applied across all bridge schools to gather information on infrastructure, classroom environment, and quality of education, guided by semi-structured observation questions.

IV. Key Finding and Discussion

4.1. Relevance, Coherence, and Context

Concerning the policy and strategic relevance, the project found highly aligned with global (SDGs), cross-national and national policies of the Republic of Korea (ROK). As the ROK-Bangladesh civil society organizations' joint international project, the project clearly sought to contributing to global educational development goals such as SDG 4 (Quality Education) and SDG 8.7 (Ending Child Labor). There are clear alignment with social policy, child labor, and education policies and sub-strategies. Especially, in Bangladesh, recent national data confirms that despite decades of progress, child labour remains a significant challenge in Bangladesh. According to the latest Bangladesh Bureau of Statistics and UNICEF survey (MICS 2025), among children aged 5–17, approximately 9.2 % are now engaged in labour, up from 6.8 % in 2019. This increase corresponds to an estimated 1.2 million more working children, underscoring a worrying reversal of what had previously been downward trends (MICS, 2025, re-cited CDR, 2025).

Within this context in Bangladesh, the results achieved by our *Bridge Education Program*, supported by KOICA take on added significance. By enrolling children in education, providing materials, meals, extra coaching, psychosocial support and awareness sessions, our program aligns with national needs particularly for children who may otherwise be at risk of labour or dropping out. Given the national increase in child labour, our success in completing primary-level courses for Bridge School students, high participation rates in counselling and extra-coaching, and widespread provision of school materials and meals suggest that Bridge Education Program is delivering meaningful protective and enabling services. Therefore, in comparison to the new national data, our results appear appropriate and even noteworthy: at a time when overall child labour is rising, our targeted interventions are contributing to education retention, rights awareness, and social protection outcomes that stand to yield important, longer-term benefits for children's development and their chances to break cycles of poverty and labour.

In regards to external consistency, there was no overlap found with international organizations (UNICEF, ILO), major civil society organizations (Save the Children, BRAC, etc.) in terms of project level, specific areas, or target areas. Synergy was created for policy cooperation through the establishment of CLEP (Child Labor Platform) with other civil society organizations (21 including Shapla Neer, Action for Social Development, and Bangladesh Labour Foundation). Further, in terms of internal consistency, there are complementary aspects found to related projects related to the Korean government's country-specific cooperation projects in Bangladesh (TVET, HRD, industry, migration, etc.), confirming its distinctiveness as a civil society cooperation project.

The project's strategies were found that it is well-aligned with local needs and contexts, effectively supporting child laborers' retention in school, enhancing parental awareness, and promoting students' personal growth. Flexible class schedules, nutritional support, psychosocial counseling, and skills training collectively created a supportive learning environment that addressed both educational and socio-economic barriers. Flexible class timings, tiffin support, and regular counseling sessions were key strategies for retaining child laborers in school. Together, these measures foster an inclusive environment, promoting consistent attendance and improving retention among vulnerable children. By mitigating barriers related to time, nutrition, and psychosocial well-being, the project strengthened both participation and learning outcomes.

Awareness campaigns and sessions effectively enhanced parental understanding of education and the risks of child labor. Awareness of educational rights among duty bearers increased from 20.26 percent at baseline

to 44.9 percent at end line, a 24.64 percentage point increase, surpassing the target of 40 percent. These findings suggest that the initiatives successfully raised awareness and encouraged parental support for their children's schooling, contributing to a positive shift in community attitudes toward education and reducing reliance on child labor. The campaigns played a crucial role in reinforcing the project's overall educational objectives.

Additionally, community and parental awareness programs contributed to transforming attitudes toward child labor and education. Through workshops, meetings, and continuous communication, parents and community members became more informed about the negative impacts of child labor and long-term benefits of education. This encouraged families to prioritize schooling over income-generating activities for their children. Overall, Parents' perception of children's right to education and the risks of child labor increased from 36.45 percent at baseline to 99.6 percent at end line, reflecting a 63.15 percentage point increase. These efforts reinforced parental commitment and sustained student engagement.

The provision of psychosocial support directly improved children's confidence, emotional regulation, and willingness to participate in school activities. Qualitative findings demonstrated:

Psychosocial support was crucial for children's well-being and learning engagement, particularly for female students. The sessions not only helped students manage stress but also fostered active participation, strengthening overall educational outcomes while addressing gender-specific needs

(FGD, Community leaders, Bridge school-8, End-line Assessment Report, 2025)

Inclusion of computer training and life skills sessions further enhanced students' motivation and aspirations beyond primary education. Practical skills such as basic computer literacy, communication, and problem-solving helped children envision future opportunities in education and employment. These experiences increased self-confidence, encouraged continued learning, and motivated students to set higher personal and educational goals. By connecting practical skill development to broader life aspirations, the project reinforced the importance of education as a pathway to personal growth and socio-economic advancement, ensuring that students were better prepared for future challenges beyond the Bridge School program.

4.2. Efficiency

All outputs presented in the PDM will be achieved by the end of November 2025. As of October 2025, all outputs presented in the PDM have been achieved early. As of the end of November 2025, the project is expected to achieve its outcomes (1,280 students completed the program) before completion. The contribution assessment and end-of-project survey results indicate that the project's contribution to the project will be readily verified.

The PDM presented during the planning stage presented key project outcomes similar to those of existing education projects, which limited the project's specificity as a KOICA citizen cooperation project (child protection and labor). To address these limitations, the evaluation team presented the following change model (existing) and revised change model. The model below was constructed by placing the outcomes of the project (Outcome) at the top, including the outcomes for child protection and reduction of child labor among the outputs being achieved through this project by ChorogUsan-EduCo.


This section presents the findings from the End line Survey regarding the key indicators outlined in the

project’s logical framework. The indicators reflect the project’s impact on children’s access to education, improvements in learning environments, awareness of educational rights, and provision of support services in the eight bridge schools.

At the time of field assessment in November 2025, all outputs presented in the PDM was achieved by the end of November. (Project Period Achievement and Management) While the initial project launch was somewhat delayed, the project progressed rapidly in 2024 and 2025. Early achievement of outputs confirmed. In next section, the report highlights the details of all outputs based on indicators.

Indicator 2.1: percentage of child laborers with improved awareness of educational rights (male/female)

The end line survey findings indicate a substantial improvement in children’s awareness regarding educational rights, reaching 41 percent overall, an increase of 25.62 percentage points from 14.98 percent reported in the baseline study, thereby achieving the project target of 40 percent. In this analysis,

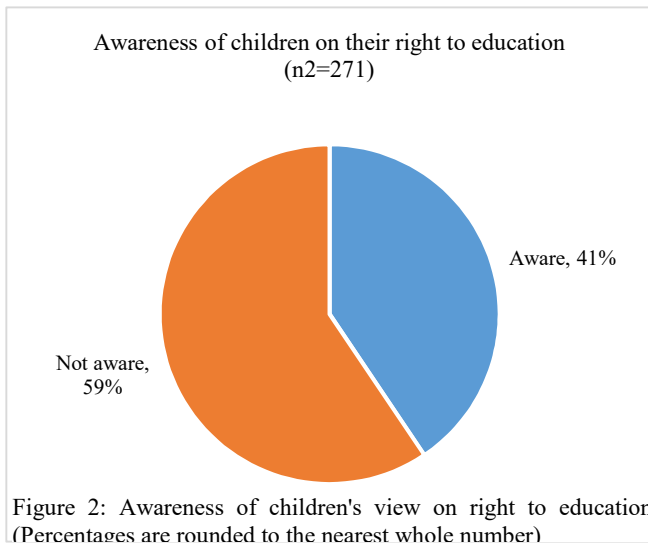

respondents were considered “aware” if they could identify at least three aspects of educational rights. In terms of awareness of educational rights, 81.2 percent of respondents reported that they had heard about the right to education. A strong majority (78.2 percent) agreed that all children should have access to education. Students also demonstrated an understanding of key rights-based principles, including education being free (39.9 percent), equal access to any school (33.2 percent), and equal opportunities for all children to receive the same type of education (19.6 percent). Although several aspects were mentioned, the idea that all children should have access to education was cited significantly more often than others.

Additionally, regarding perceptions of the right to education for working children, most respondents believe that working children also have the right to education, with 76.0 percent agreeing largely. The agreement was higher among girls (86.8 percent) than among boys (65.2 percent). Around 22.5 percent felt that this right exists to some extent, while a small proportion of boys (3.0 percent) perceived it to a poor extent (detail in annex Table 3).

Indicator 2.2: percentage of duty bearers with improved awareness of educational rights (male/female)

A significant improvement in awareness was also observed among duty bearers, with the percentage rising from 20.6 percent at baseline to 60.8 percent at end-line, exceeding the project target by about 20 percent.

The survey findings indicate a notable increase in duty bearers' understanding of children's educational rights. The same analysis approach as the baseline study was followed to ensure consistency. End-line study reveals that 87.9 percent of respondents recognized that all children should have access to education. Additionally, 41.1 percent of duty bearers understand that all children should receive a similar type of education. Duty bearers also demonstrated a strong understanding of the broader benefits of education, including its role in reducing poverty (87.5 percent) and preventing child labour (67.9 percent). Overall, the indicator shows meaningful improvement; duty bearers are increasingly aware and supportive of children's education (details in annex Table 19 and Table 4).

Output 1.1 Bridge Schools equipped with infrastructure

Indicator 1.1.1: Number of bridge schools equipped with infrastructure

The indicator presents key output-level indicators, showing end-line data, targets, and observed changes. For the indicator “# of Bridge Schools equipped with infrastructure,” the end-line data shows 8 schools, matching the target of 8 schools, indicating that the target has been fully achieved. No change in calculation is necessary as the target was met.

Output 1.2 Integrated programs operating in Bridge Schools

Table 1: Indicators Table of Output 1.2

Indicator	Baseline	End-line4	Target	Comments
	1.2.1 Number of children enrolled in the bridge education program			
Boys	0	400	400	100% achievement
Girls		400	400	
Total	0	800	800	
	1.2.2 Number of children received psycho-social counseling (boys/girls)			
Boys	0	973	120	Over achievement
Girls	0	1023	120	
Total	0	1996	240	
	1.2.3 Number of slow learners receiving extra coaching (boys/girls)			
Boys	0	1094	600	Over achievement
Girls	0	1087	600	
Total	0	2181	1200	
	1.2.4 Number of students who received school materials and meals (boys/girls)			
Boys	0	1190	1,200	Target achieved
Girls	0	1210	1,200	
Total	0	2400	2400	

⁴ Data source: Semi Annual Progress Report 2025

Indicator 1.2.1: Number of children enrolled in bridge education program

The project achieved 100% of the enrollment target, with all 800 intended children enrolled. Among 265 surveyed respondents (135 female, 130 male), the primary sources of information about the program were neighbors or relatives (138) and teachers (109). Most families (240 of 265) enrolled only one child, while 24 families enrolled two children and one family enrolled three. The main reason for admission, cited by 242 respondents, was the NGO's superior facilities, followed by an understanding of the importance of education (181) and a desire to secure a bright future for children (153), especially emphasized by female respondents (90 versus 63 male). These findings indicate that community networks and the NGO's reputation were key drivers of enrollment.

Indicator 1.2.2: Number of children received psychosocial counseling

Survey findings indicate that 97.8% of children received psycho-social counseling, with varying levels of participation: 48% always attended, 31.7% often attended, 13.7% attended occasionally, and 3.3% attended rarely, while 2.2% reported not receiving counseling. Document review further shows that 1,996 children (973 boys and 1,023 girls) received counseling, along with an additional 240 children (120 boys and 120 girls) who participated in a structured counseling session. KII insights highlight that many children are growing up in challenging environments, resulting in increased aggression and behavioral issues; therefore, teachers noted that psycho-social counseling was provided to most children to help address these concerns and support their emotional well-being.

Indicator 1.2.3: Number of slow learners receiving extra coaching

Survey findings show that 84.5% of children attend extra coaching classes, while 15.5% do not attend. Document review indicates that 2,181 slow learners (1,094 boys and 1,087 girls) received extra coaching, compared to the target of 1,200 students (600 boys and 600 girls). KII discussions with teachers revealed that many students face academic challenges because they rely solely on classroom learning. To address these learning gaps and strengthen foundational skills, a larger number of students have been engaged in extra coaching sessions.

Indicator 1.2.4: Number of students who received school materials and meals

Survey findings show that 99.6% of students received school materials, while only 0.4% reported not receiving them. Similarly, 99.6% of students reported receiving meals daily, and 0.4% stated they received meals 3–4 times a week. Document review indicates that a total of 2,400 students (1,190 boys and 1,210 girls) received school materials and meals, exceeding the target of 2,400 students (1,200 boys and 1,200 girls). This demonstrates that the target has been fully achieved. However, the number of male students fell slightly below the target because enrollment of boys in Bridge Schools has been lower than that of girls since Year 2.

Indicator 1.2.5 # of 8 bridge school students who have completed the primary education course (who passed the exam for next grade) / 2nd year (Grade 3), 3^{year} (Grade 4,5/per 6mont

- Year - 2: Document review shows that 395 male and 405 female students (total 800 students) successfully completed the 2nd-year (Grade 3) exams.
 - Year - 3: The same numbers were recorded (395 male and 405 female students, total 800 students) successfully completed the Grade 4 exams.
 - Overall, 640 students (320 male and 320 female) have been verified to date against the target.
-

Indicators 1.3.1: Number of 3-year condensed curriculum developed

The end line data shows that 1 condensed curriculum has been developed, which meets the set target of 1. This indicates that the target for developing the 3-year condensed curriculum under the Bridge Education Program has been fully achieved. No change in calculation is required as the target was met.

Indicators 1.3.2: Number of teachers trained on bridge education program

Document review indicates that 72 teachers have been trained under the Bridge Education Program. Although this is still below the overall target of 96 teachers, progress demonstrates steady advancement toward the goal. Continued efforts are underway, and the program is on a positive trajectory to achieve full target completion.

*(Output 2.1) Improved awareness of educational rights
among child labourers and community duty bearers*

Table 2: Indicators Table of Output 2.1

Indicator	Baseline	End-line5	Target	Comments
2.1.3 Number of bridge school students who participated in awareness sessions (boys/girls)				
Boys	0		1,200	Ongoing activities
Girls	0		1,200	
Total	0	2211	2,400	
2.1.4 Number of parents who participated in sessions to improve awareness of children's rights and educational rights (male/female)				
Fathers	0	858	1,200	Over achievement
Mothers	0	1,745	1,200	
Total	0	2,603	2400	

Indicators 2.1.1: Number of campaigns and anniversary events to advocate child labourer's right to education

Document review shows that 10 campaigns and anniversary events were conducted against a target of 12. As these activities are still ongoing, the final number may increase by the end of the project period. The change cannot be calculated at this stage due to the continuation of activities.

Indicators 2.1.2: Number of employers and local residents who participated in sessions to improve the awareness of educational rights of child labourers

Document review indicates that a total of 2965 employees and local residents participated in awareness sessions, exceeding the target of 2,160 participants. This reflects an overachievement of the target set. The end-line assessment team's KII findings further reveal that the project team successfully motivated community members and employers to attend the sessions, which strengthened their understanding of child labourers' educational rights. This initiative not only enhanced individual knowledge but also contributed to fostering wider community awareness. Moreover, participants are now encouraging others in the community to become more informed, indicating positive ripple effects.

Indicators 2.1.3: Number of bridge school students who participated in awareness sessions

Survey findings show that 94.1% of Bridge School students participated in awareness sessions on children's rights and educational rights, with only 5.9% reporting no participation. Document review further indicates that 2,211 students have taken part in these sessions to date, against a target of 2,400 students (1,200 boys and 1,200 girls). While participation was slightly below the numerical target at the time of assessment, the sessions were still ongoing during data collection. As a result, the remaining coverage is expected to improve, and overall participation is on a positive trajectory toward meeting the program goal.

Indicators 2.1.4: Number of parents who participated in sessions to improve awareness of children's rights and educational rights

Survey findings show that 86.4% of parents participated in awareness sessions on children's rights and educational rights, while 13.6% did not participate. Document review indicates that 2,603 parents attended the sessions (858 men and 1,745 women), exceeding the target of 2,400 parents (1,200 men and 1,200 women). During KIIs, teachers explained the relatively lower participation of male parents, noting that most men are occupied with work during daytime hours when these sessions are typically held, which limited their availability to attend.

Indicators 2.2.1: Number of people who participated in CLCLMC

Document reviews by both Korean evaluation results and end-line assessment results have confirmed that 264 participants took part in CLCLMC activities, fully achieving the established target of 264 participants.

Indicators 2.2.2: Number of monitoring visits at workplace and household

Document reviews by both Korean evaluation results and end-line assessment results have confirmed that 88 monitoring visits conducted against a target of 96. Monitoring activities are still ongoing; therefore, the final number may increase as the project continues.

Indicators 2.2.3: Number of CLCLMC members participated in sharing meetings

Document reviews by both Korean evaluation results and end-line assessment results have reported that 132 participants, exceeding the target of 48. The activity remains ongoing. Although the target was based on meetings with 16 members, participation expanded to include CLCLMC and SMC members from all schools, contributing to the higher number.

Indicators 2.3.1: Number of participants in the joint workshop to ensure the educational rights of child labourers

Document review shows 325 participants, well above the target of 120. The activity is still ongoing, and final participation may increase further.

Indicators 2.3.2: Number of policy proposal to provide educational services for child labourers

No policy proposal has been finalized yet against the target of 1. The activity is ongoing, and the proposal is expected to be developed as the project progresses. In regards to efficiency of the implementation mechanism, the ChorogUsan for children-EduCo (Children's Foundation Alliance)- ESDO (Eco-Social Development Organization) collaborative system was confirmed to be operating efficiently, based on smooth communication and mutual expertise, with a focus on field operations. However, existing project documents (various reports) do not clearly reflect this collaborative system, which may lead to some confusion. Therefore, improvements are needed at the reporting level. The ChorogUsan for children-EduCo (Children's Foundation Alliance)-ESDO (Eco-Social Development Organization) collaborative system was confirmed to be operating efficiently, based on smooth communication and mutual expertise, with a focus on field operations. However, existing project documents (various reports) do not clearly reflect this collaborative system, which may lead to some confusion. Therefore, improvements are needed at the reporting level.

4.3. Effectiveness

4.3.1. Key Outcomes

The project aimed to improve the learning environment for child laborers and enhance awareness of children’s educational rights. Across baseline, target, and end-line phases, data indicate substantial progress in access to education and related support services.

Outcome 1: Improved learning environment of basic education tailored to the characteristics of child laborers

Indicator 1.1: Percentage of bridge schools approved by government as non-formal facilities

The end-line data shows that 100% of Bridge Schools received government approval as non-formal educational facilities, fully meeting the target of 100%. This reflects complete achievement of the indicator, with no change in calculation required since the target was attained.

Indicator 1.2: Percentage of bridge school students who have completed the bridge school course

Substitute Indicator: Number of students who have participated in the graduation exam

Table 9: Outcome 1 indicator 1.2

Indicator	Baseline	End-line	Target (%)	Change
1.2 Percentage of bridge school students who have completed primary education	0	-	70	Not been determined yet

The project has been running for three years, with a total of 800 students currently enrolled across eight bridge schools. As the academic year in Bangladesh concludes in December, none of the students have officially completed their primary education at the time of this evaluation. However, all 800 students have participated in the graduation exam, serving as a strong proxy for measuring progress toward completion. Among the 271 surveyed learners, every student expressed a clear intention to complete their primary education by the end of 2025. This high level of motivation, combined with full participation in the graduation exam, indicates strong progress toward the project’s target.

The project aims for 70 percent of students to complete primary education during its implementation period. Although formal completion data will only be available after the academic cycle ends, the current participation and expressed commitment suggest that the project is on track to meet—or come close to—its completion target once results become available early next year.

Outcome 2: Strengthened social awareness and institution of educational rights of child laborers

The following table presents the baseline and end line percentages of child laborers with improved awareness of educational rights, along with the project target and the changes achieved to date. Awareness of educational rights increased notably among all groups. For child laborers, it rose from 14.98 percent at baseline to 40.6 percent at end line, a 25.62 percentage point increase, slightly exceeding the 40 percent

target. Among duty bearers, it improved from 20.26 percent to 60.8 percent, a 40.54 percentage point rise, surpassing the target by a wide margin. Overall performance indicates a positive improvement in raising awareness among students and duty bearers.

Table 10: Indicators table of Outcome 2

Indicator	Baseline (%)	End-line (%)	Target (%)	Change (%)	Remarks
2.1 % of child laborers with improved awareness of educational rights (male/female)					
Male	10.57	41.5	40	25.62 (↑)	Target achieved; awareness measured as ability to identify at least 3 aspects of educational rights.
Female	4.41	39.7	40		
Total	14.98	40.6	40		
2.2 % of duty bearers with improved awareness of educational rights (male/female)					
Male	11.01	60.8	40	40.54 (↑)	Exceeded target; strong recognition of children’s right to education and related benefits.
Female	9.25	60.7	40		
Total	20.26	60.8	40		

The evaluation results, including the end-line assessment, highlight the extent to which the project achieved its intended outcomes, explore the drivers behind successes, analyze the challenges that contributed to shortfalls, and identify unexpected outcomes that shaped the overall impact. Together, these discussions provide a deeper understanding of the project's performance, sustainability, and relevance within the local context.

Both the results from the evaluation and end-line assessment have found out that the project provided comprehensive psychosocial support, with 262 children receiving counseling. Girls demonstrated higher participation and perceived effectiveness, with 86 attending “always” versus 44 boys, and 113 girls finding sessions helpful largely compared to 69 boys. According to end-line assessment results, extra coaching reached 229 students, mainly through short sessions under two hours; boys attended longer sessions more frequently, but girls reported greater benefit, with 87 rating the coaching as highly helpful versus 55 boys. Provision of school materials and daily meals was nearly universal, with 270 students receiving writing materials and meals, 269 receiving textbooks and uniforms, and 267 receiving bags. Most students (234) found these resources very useful, with girls (131 of 136) reporting stronger appreciation than boys (103 of 135), highlighting gendered perceptions of resource utility. Moreover, according to end-line assessment results, awareness of educational rights improved from 14.98% at baseline to 40.6% at end-line, meeting the target. Most respondents (81.2%) recognized the right to education, and 78.2% believed all children should attend school.

Awareness sessions engaged 996 boys and 1,015 girls, slightly below the target, yet over 90% of children and parents reported improved understanding, with female parent participation particularly high due to men's work commitments. Overall, the project effectively enhanced enrollment, psychosocial support, access to materials and meals, and awareness of educational rights, particularly among girls. Despite the absence of formal completion data, students' strong motivation, improved awareness, and active participation indicate significant progress toward sustaining education and reducing child labor,

demonstrating the project's overall success in achieving its objectives.

One of the critical findings have shown in the evaluation team's field investigation, which is supported by the end-line assessment survey is the fact that children's earnings constitute only a small fraction of total household income, and households rely primarily on adult earners. While some older children may contribute substantially to the household income, their individual earnings are generally insufficient to match the household-level expenditures, which are necessary to meet family needs in urban slums. Overall, the comparison shows that children's income complements but does not replace household income, and expenditures are supported mainly by the larger household income, with children's contributions forming a minor yet important supplement, particularly in higher-earning boys.

The data in the below Table shows that respondents' household earnings are concentrated in specific ranges. Most households earn between BDT 20,000 and 29,999 per month, with 22.6% earning BDT 20,000–24,999 and 30.6% earning BDT 25,000–29,999, making these the most common income levels among the surveyed population. Earnings below BDT 15,000 are relatively rare (1.5%), and only a small fraction of households earn above BDT 40,000 (2.3%).

Table X: Respondents' monthly household income range

Response	Monthly Income (% of Respondents)	Monthly Expenditure (% of Respondents)
<15000	1.5	5.7
15000-19999	13.2	24.5
20000-24999	22.6	31.3
25000-29999	30.6	18.9
30000-34999	18.1	10.2
35000-40000	11.7	7.5
>40000	2.3	1.9
Total	100.0	100.0

The distribution of children's monthly income shows in the below table that earnings are generally lower than household income. Most children earn between 1501–3000 BDT per month, with 21.5% earning 1501–2000 BDT, 19.8% earning 2501–3000 BDT, and 24.3% earning above 3000 BDT, while a large proportion of girls earn in the lower ranges (1001–2000 BDT) and boys are more concentrated in the higher ranges (2501+ BDT), highlighting a clear gender disparity.

Table X: Children income range

Response	Girls	Boys	Total (n2'=177)
<500	3.4	0.0	1.7
500-1000	14.9	6.7	10.7
1001-1500	23.0	4.4	13.6
1501-2000	29.9	13.3	21.5
2001-2500	4.6	12.2	8.5
2501-3000	10.3	28.9	19.8
>3001	13.8	34.4	24.3
Total	100.0	100.0	100.0

4.5. Impact (Readiness)


In this section, the evaluation results are highlighted regarding whether the project has ultimately contributed to enhancing basic education rights of child laborers subjected to the project in the targeted slum areas in Dhaka.

Impact (Readiness): Enhanced basic education rights of child laborers subject to projects in Dhaka

Indicator: Percentage of 8 bridge school students enrolled in lower secondary school

First, while no students had formally completed primary education by the end-line assessment due to the academic calendar, all 271 surveyed students expressed intent to complete their studies by 2025, demonstrating strong motivation toward achieving the project target of 70% completion. Additionally, according to end-line assessment results, bridge school enrollment data from 265 respondents show that the most families (240) enrolled in a single child, primarily influenced by neighbors (138) and teachers (109). The analysis examined the likelihood of bridge school students continuing their education in lower secondary schools rather than focusing solely on actual enrollment. As the evaluation was conducted before December, when final examinations are usually held in Bangladesh, the actual enrollment status could not be accurately determined. The end-line assessment findings show that most students (86.3%) expressed a strong willingness to be admitted to high school after completing primary education in the Bridge School. Specifically, 97.1% of girls and 75.6% of boys reported that they were willing “to a great extent.” However, a small proportion of boys indicated lower levels of willingness 8 students (5.9%) responded “to a poor extent,” while 3 students (2.2%) said “not at all.”

Figure 3. Contribution Analysis

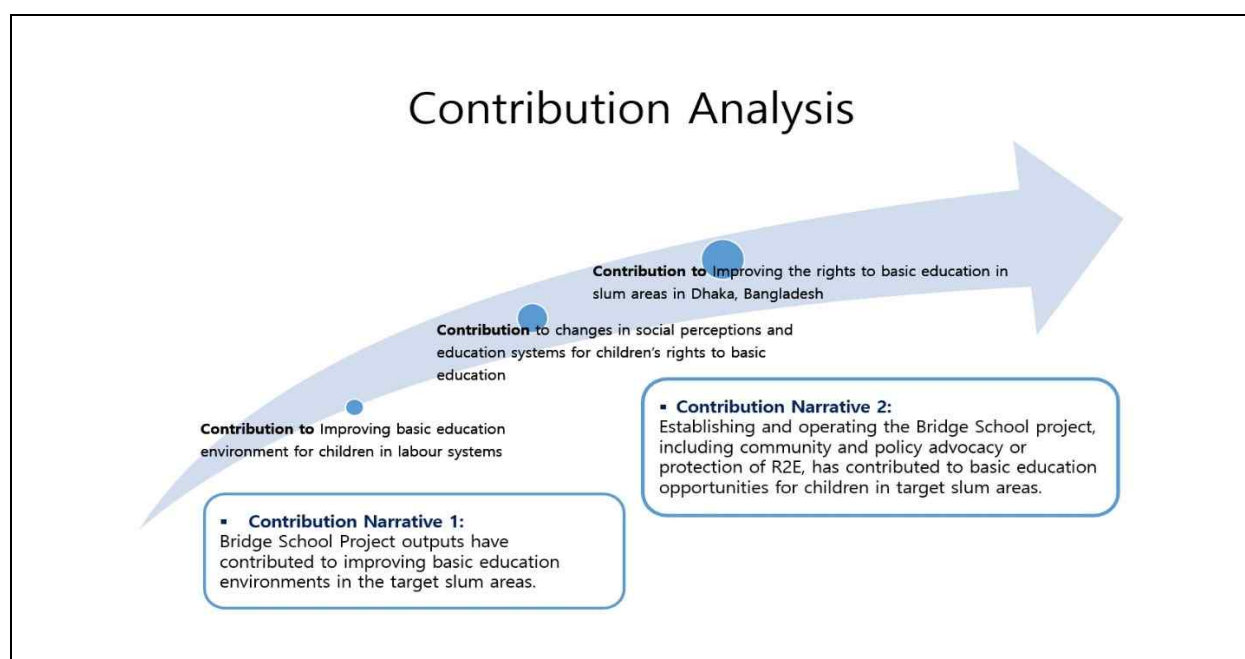

* Developed based on ToC and PDM (2025)

As for the outputs-outcome contribution claim for *improving the basic education environment for children in labour systems*, have been clearly proven in the section on efficiency and effectiveness. Likewise, the outcomes-impact contribution claim for *improving the rights to basic education in slum areas in Dhaka* is clearly proven and cross-checked by external specialists. However, the contribution of outputs, which are related to improving basic education environments solely, cannot provide the outcomes and impacts created. The evaluators and third-party specialists both agreed that community and policy advocacy or protection of R2E have been undervalued and less highlighted for contributing to basic education opportunities for children in target slum areas.

Regarding the unexpected outcomes and their implications, the project yielded several unexpected outcomes, both positive and negative, which had important implications for student participation, community engagement, and educational access. While interventions successfully increased enrollment and engagement, challenges related to safety and accessibility continued to affect some students. Families help their children to get more motivated in their studies, as 44.3 percent of students responded that family encourages them to enroll in school. The assessment result shows that the primary motivation for joining school among children is the desire to continue their education (88.2%), reflecting strong personal aspirations for learning.

Additionally, 57.2% of respondents joined to gain basic reading and writing skills, while 44.3% were motivated by family encouragement. Students contributed as peer educators, raising awareness about education and child rights in their communities. They shared personal learning experiences and motivated other children and parents to value schooling, helping to shift community perceptions about child labor and education. One student described,

I try to help other children and their parents understand the importance of the right to education. For example, there's a girl in my neighborhood who used to work as a house helper and didn't go to school. I talked to her parents and explained why education is important.

(IDI, Female, Student, Bridge School-5, End-line Assessment Report, 2025)

Initially, employer visits were very difficult. However, this year, with the project already well-known [in the community], home and employer visits have become less difficult.

[In particular], in areas with frequent return visits, we are meeting new employers. We have observed that children work fewer hours, from approximately six hours to four to five hours.

Some students in my community have successfully returned to school, and the program is having a positive impact because awareness of children's rights within the community is obviously changing. (FGI, Male, CLCMC member, Field Evaluation Report, 2025)

I feel rewarded as a member of CLCMC when seeing a child return to school thanks to the members' efforts is the most rewarding moment. (KII, Female, CLCMC member, Field Evaluation Report, 2025)

A large proportion (77.5%) also reported that better facilities provided by NGOs encouraged them to enroll, underscoring the importance of institutional support. During the evaluation field trip, the CLEP's joint effort was found meaningful regarding the linkage between various outcomes and impact. Following the inactivity of existing child labor networks (e.g., JSF), the evaluation team has found that CLEP was launched to address the need for a new civil society-led collaborative effort in Bangladesh in 2019-2020. The CLEP aims to bridge the gap in coordination and policy alignment between the government, the ILO, and NGOs. Several organizations voluntarily formed CLEP to address child labor issues and engage in policy advocacy and capacity-building activities. Operating on a voluntary basis rather than a project-based approach, CLEP has established itself as an informal policy advocacy coalition, serving as a bridge between the government and civil society, and it currently 21 organizations⁶ are being participated.

We, members of CLEP, prioritized institutionalizing the platform and ensuring its sustainability. This includes registering an independent legal entity, establishing a permanent secretariat, and establishing a fund. Collaboration with international partners, including those from Korea and Europe, is welcomed. While financial support is appreciated for the benefits for children and international cooperation, the platform's independence must be maintained.

(KII, Male, CLEP member, President of EduCo, Field Evaluation Report, 2025)

Through CLEP, civil society began to communicate its position through review of the government's National Action Plan (NAP) and participation in the Labor Reform Committee. It monitors and advocates for the implementation of ILO conventions and makes policy recommendations on multiple vulnerable areas, including child labor, sexual violence, and human trafficking. CLEP is defined as a catalyst for policy change and exerts influence on both the government and the media. The project to promote basic education rights for working children in the slums of Dhaka, Bangladesh, implemented by KOICA and the ChorogUsan for children, has been confirmed to have provided a crucial foundation for the expansion and development of CLEP.

Key priorities for 2025-2030 will focus on strengthening policy advocacy, supply chain monitoring, and monitoring the implementation of ILO conventions—all of which can be implemented independently by a single organization across a few workplaces.

(KII, Male, CLEP member, Save the Children Child Labour Focal Person, Field Evaluation Report, 2025)

Despite these positive outcomes, accessibility barriers also affected some children, particularly those living far from school. Long distances and lack of affordable transportation made commuting difficult, causing physical fatigue, which sometimes affected punctuality and overall participation in school activities.

⁶ UN Agency: UNICEF. INGO: World Vision, Good Neighbors, Shapla Neer, Caritas, International Rescue Committee(IRC), Educo · National NGO: Aparajeyo Bangladesh, Bangladesh Shishu Adhikar Forum(BSAF), Bangladesh National Women Lawyers Association(BNWLA), Development Communication Network(DCN), Bangladesh Institute of Labour Studies(BILS), Grambangla Unnayan Committee, INCIDIN Bangladesh, Manusher Jonno Foundation(MJF), Nari Maitree, Solider Suisse, Terre des hommes Foundation, Action for Social Development(ASD), Bangladesh Labour Foundation(BLF), ESD

4.6. Sustainability

Although overall willingness was high, the data reveal a gender gap: girls expressed greater aspiration for continued education, but qualitative findings suggest that practical barriers—such as financial hardship, household responsibilities, and safety concerns may reduce their actual transition rate. FGD and IDI discussions further supported this, with parents acknowledging their children’s improved motivation and learning progress but highlighting persistent economic pressures and early involvement in income-generating activities that could hinder real enrollment outcomes. If the project highlights the child protection aspects not highlighted in Phase 1, it will be modeled as a unique ChorogUsan for children project for child laborers.

- Sustainability (School Space Rental Costs): The on-site survey clearly confirmed the legitimacy and necessity of locating schools within slum areas. Furthermore, it was confirmed that government support for space (e.g., the Ministry of Labor and Employment and the Ministry of Education/Office of Education/Office of Non-Formal Education) was not realistically feasible given the non-formal education system (the government does not provide space to non-formal education institutions).
- Sustainability (Meals): For school meals, which require verification in terms of sustainability, a decision will be made after further investigation, as it appears to have a direct correlation with business effectiveness (enrollment and attendance of children from working and poor families).
- Sustainability (Bangladesh Government Cooperation): Cooperation with the Ministry of Labor and Employment is excellent, and collaboration with the Ministry of Basic and Mass Education is ongoing, including the provision of free textbooks at the local level (tana). Due to the change in government in the first half of 2026, follow-up communication is essential to ensure correspondence regarding related support.

The project has laid a strong foundation for sustainability and local ownership by fostering community engagement, building teacher capacity, providing material support, and raising awareness of children’s rights, although challenges remain regarding government integration and long-term institutional support. The project successfully strengthened social norms against child labor by raising awareness of children’s rights and education. High proportions of students are aware of the right to education (81.2%) and that schooling is free and compulsory (86.3%). The results below show that a majority (76.0%) believe working children also have a right to education, with girls showing stronger conviction (86.8%) than boys (65.2%).

The project promoted emerging local ownership through active participation of CLCLMC and SMC committees, which supported school management, monitored student attendance, and encouraged educational activities. A KII participant during the end-line assessment shared that: CLCLMC committee members regularly meet to discuss student attendance and school issues.

We are now more confident in taking decisions and supporting children’s learning. We organize meetings, monitor school activities, and coordinate with teachers to ensure children remain enrolled and engaged.


(KII, CLCLMC Member, Bridge school-2, End-line Assessment)

Despite these successes, government recognition and integration of Bridge Schools into local education planning remain limited, posing challenges for long-term sustainability. According to the assessment, although the project improved access to education for child laborers and marginalized children, the lack of formal government endorsement restricts opportunities for scaling or institutional support. Without policy alignment, continuity beyond the project duration is uncertain, and collaboration with mainstream schools is constrained. Strengthening government engagement and formal integration into local education systems is critical to ensure sustained educational pathways for students, broaden the program's impact, and enhance the institutionalization of successful project strategies. Access to free education, learning materials, and financial support played a crucial role in enabling students from low-income families to continue their studies. Many students faced residential constraints due to the loss of their parents. According to field observations by both Korean and Bangladesh teams, most students are dependent on project assistance.

V. Analysis of Enablers and Constraining Factors

Overall, the evaluation findings demonstrate that the Bridge Education Project has made significant progress in enhancing. In this section, Enablers and Constraining Factors. First of all, the suggested theory model has been further expanded, and it will be explained in the section on impact and sustainability. The evaluation team suggests that the impact does not need to be modified. However, the project team suggests that a more comprehensive ToC should include three outcome areas: (i) Outcome 1. Improved Basic Education Environment for Children in Labour Systems; (ii) Outcome 2. Improving Protection against Hazardous Work for Children; (iii) Outcome 3. Stakeholders' Perception Changes for the Rights to Education of Children.

Figure X. Theory of Change-As-is Model

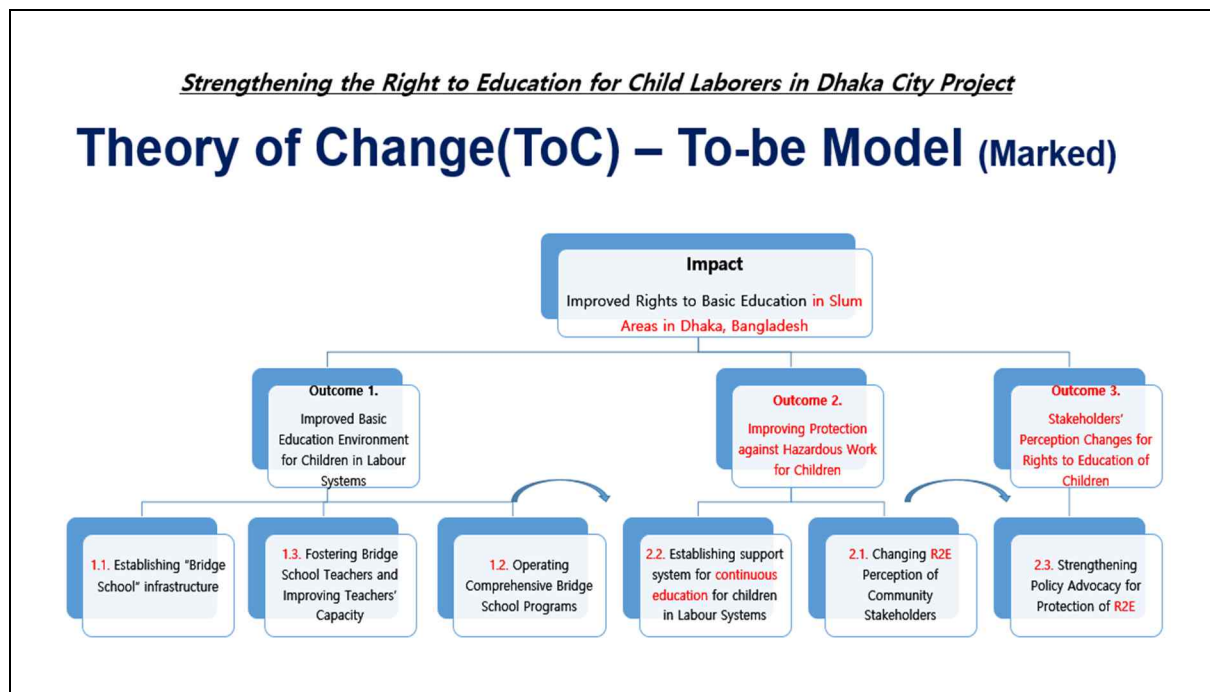

* Developed based on existing Project PDM (2025)

5.1. Enablers

The project's combined interventions, including free educational materials, meals, counseling, and parental engagement, have significantly improved students' attendance, motivation, and overall educational outcomes. The perception that education materials should be provided free of charge showed a significant increase over the project period. At baseline, only 5.78 percent of respondents endorsed this view, which rose to 20.3 percent at end line, reflecting a 14.52 percentage point increase. In response to receiving schools meals, all 800 students (100 percent) received school meals by the end line, fully meeting the project target. This reflects the effective implementation of nutrition support, enhancing attendance and learning outcomes (CRD 2025).

While most students received assistance and protection from government and non-governmental organizations, 28.4 percent reported no support, indicating gaps in safety coverage. According to end-line assessment results, the proportion of child laborers with improved awareness of educational rights increased from 14.98 percent at baseline to 37.6 percent at end line, reflecting a 22.62 percentage point increase,

approaching the project target of 40 percent. This substantial improvement demonstrates the effectiveness of the project's interventions in raising children's understanding of their educational rights and promoting their access to schooling. The project's provision of uniforms, learning materials, meals, and psychosocial counseling has eased financial burdens for families and strengthened students' confidence and engagement. The qualitative findings highlighted the educational outcomes and their positive impact on reducing child labor while increasing educational opportunities for children, as one child laborer shared:

If students like us get free education and learning materials, it will be much easier for us to move on to lower secondary school. We receive meals six days a week, and counseling sessions to relief our stress

(IDI, female, Age 13, student, Bridge school-3, End-line Assessment Report, 2025)

Moreover, the meal program has improved children's health, attentiveness, and eagerness to attend school, while the combined support system of learning materials, uniforms, and counseling has created a more inclusive and supportive learning environment. Students receiving these resources and emotional support became more confident, engaged, and committed to their studies. Additionally, counseling sessions and structured routines further enhanced students' confidence, behavior, and mental well-being. Psychosocial support helped children overcome fear and anxiety, enabling active participation in class and interaction with peers and teachers.

Before coming to school, I was afraid to talk to people. I would remain quiet and did not want to participate in class activities. Sometimes I even felt nervous walking to school alone. After joining the Bridge School, the counseling sessions helped me understand how to handle my fears

(IDI, female, Age 12, child labor, Bridge School-2, End-line Assessment Report, 2025).

Overall, these activities increased parental understanding of schooling, addressed misconceptions, and encouraged positive attitudes toward education. Committees acted as a bridge between schools and families, identifying reasons for reluctance to send children to school, providing counseling, and monitoring attendance. The combination of home-based engagement and community advocacy created a supportive environment, strengthened parental responsibility, and promoted sustained student attendance and motivation.

4.7. Constraining Factors

The Bridge Schools faced several internal and external challenges that limited the full achievement of project targets, including infrastructural constraints, economic pressures on families, migration, community-level risks, and political instability. Economic hardship among families created pressures that sometimes-forced children to return to work instead of continuing education. The percentage of bridge school students continuing to work decreased from 99.12 percent at baseline to 65.3 percent at end line, reflecting a 33.82 percentage point. Financial constraints often limited families' ability to support prolonged school attendance, prompting children to engage in income-generating activities to meet household needs. These data highlight the importance of the Bridge Schools' flexible learning approach in enabling working children to continue education while supporting family livelihoods.

Thus, these factors affected student attendance, learning quality, and overall engagement, despite the project's supportive interventions. The CLCLMC focused on extending the curriculum duration from 6 to 9 months will provide students with adequate time to grasp lessons, practice skills, and achieve stronger learning outcomes. Limited classroom space and inadequate storage for learning materials were significant internal challenges. Field observations revealed that each school had only two classrooms, constraining teaching and learning by making it difficult to accommodate all students comfortably and organize educational resources efficiently. The lack of proper storage also risked the durability and accessibility of materials, potentially affecting the quality of education delivered. The qualitative findings stated the challenges regarding the attainment of educational facilities, and one respondent explained:

The classrooms are small, so it becomes difficult to accommodate all the students. If the rooms could be increased, then all the students could sit comfortably. A well-furnished room should be used to store books and other pedagogical materials. Otherwise, those get damaged.

(FGD, students, Bridge School-5, End-line Assessment Report, 2025)

According to end-line assessment results, while the schools provided a generally safe environment, infrastructural limitations affected daily student experiences. Insufficient handwashing facilities emerged as a major concern, limiting students' ability to maintain hygiene. Observations and teacher reports indicated that each school had only one handwashing section, often inadequate for the number of students, causing frequent shortages of soap and water. Additionally, migration of families created another significant barrier to educational continuity, as frequent relocation interrupted students' attendance and progress.

Also, community-level harassment and discouragement, particularly toward girls, have also reported that it had affected attendance and participation. Despite project interventions, some students faced social and safety risks that hindered engagement. Negative comments and harassment from community members initially affected children's sense of security while traveling to school. To address these risks, parental accompaniment and protective measures were implemented, enabling students to attend classes safely and participate in learning activities. These challenges underline the ongoing need for measures to ensure a safe, inclusive, and encouraging environment for all children, particularly the most vulnerable.

VII. Conclusion and Recommendation

Overall, the evaluation findings demonstrate that the Bridge Education Project has made significant progress in enhancing educational access, awareness, and well-being of working children in Dhaka's slum areas. The project successfully achieved or exceeded most of its quantitative targets particularly in enrollment, psychosocial support, and awareness raising among children and duty bearers while also generating strong qualitative evidence of positive behavioral and attitudinal change among students, parents, and community members. Despite existing challenges such as infrastructural limitations, economic constraints, and mobility of families, the project's integrated interventions free educational materials, meals, counseling, and community engagement collectively contributed to improved motivation, attendance, and learning outcomes. The overall impact indicates that the project has established a strong foundation for sustaining educational rights and creating an enabling environment for the continued education of child labourers beyond the project's life cycle.

The following recommendations are proposed based on the both Korean evaluation team and Bangladesh end-line assessment team. The findings to strengthen sustainability, inclusiveness, and the overall effectiveness of the Bridge Education Programme.

- Strengthen parental and community engagement to ensure sustained monitoring and accountability in children's education
- Institutionalizing regular home visits, awareness sessions, and committee-led monitoring will deepen local ownership and accountability. Strengthening coordination among teachers, parents, and committees such as CLCLMC and SMC will further improve attendance and retention. These actions will ensure that families remain committed to education over child labour.
- Implement gender-sensitive safety measures to promote secure access and equal participation in education. Developing community-based safety committees, ensuring safe commuting routes, and conducting awareness activities on gender-based harassment will create a secure environment for all students, especially girls. Engaging parents and local leaders in these measures will strengthen community confidence and encourage regular attendance.
- Strengthen policy advocacy and collaboration with government authorities to ensure institutional recognition and sustainability. Close collaboration with local education offices and alignment of bridge school operations with national education frameworks will enhance policy-level support and long-term sustainability. This approach will also facilitate government funding and formal recognition.
- Extend the curriculum duration from six to nine months to strengthen learning outcomes and comprehension. Extending the curriculum period will provide students with adequate time to understand lessons, practice key skills, and achieve better academic performance. A longer duration will also reduce pressure on learners and allow teachers to ensure deeper comprehension and retention.

The evaluation team verified the multifaceted and clear achievements of Project Phase 1 through a variety of quantitative and qualitative data. To ensure the sustainability of Phase 1 performance and ensure the effective launch of Phase 2, the team proposes the following considerations.

- First, it is necessary to emphasize the policy and institutional contributions related to the right to education and child labor, which were included as outputs of the first phase of the project. If the second phase is expanded, it will need to be linked to policy outcomes. Therefore, we propose highlighting and including in the project model the achievements of policy and institutional

improvements, such as expanding the role of the Child Labor Eradication Platform (CLEP) to enhance the right to education and strengthening the role of the Community-Led Child Labor Monitoring Committee (CLCLMC). In particular, ChorogUsan for children, in collaboration with Educo, has successfully implemented a system for monitoring child labor in local communities, a unique system for the Bangladeshi government (Ministry of Labor and Employment) outside of large corporations. The organization proposes strengthening the school-community linkage model in the future.

- Considering the current compulsory education age under Bangladeshi law, ChorogUsan for children and Educo propose contributing to policy and institutional improvements that expand the age of primary education and the scope of education provision. In particular, through this first project, ChorogUsan for children secured a civil society space that can contribute to institutional improvements through collaboration with the Child Labor Eradication Platform (CLEP), which Educo leads and collaborates with 21 organizations, including Save the Children, Educo, BSA, ActionAid, SOS, and Good Neighbors. We propose that future business models incorporate institutionalized achievements to address child labor issues. ChorogUsan for children, leveraging the opportunity it gained through Educo's local capabilities to participate in this network, proposes leveraging this opportunity to build a national child labor eradication platform and develop a business model for child labor.
- Third, we propose developing the Bridge School model, a specialized education program designed to address child labor issues, a key focus of the ChorogUsan for children, and implementing it in several Asian and African countries. Specifically, if ChorogUsan for children considers expanding its public-private strategic initiative in Bangladesh through collaboration with public institutions, the scope of the project should be designed to expand educational opportunities and curricula. If expanded into a strategic project in the field of civil society cooperation, we recommend actively considering linking it with national systems, including the establishment of a national digital platform for child protection and expansion of the right to education, secondary-level vocational training, and skills and digital literacy.

VI. Appendices

A. List of Evaluation Questions (Detailed)

Efficiency

- (Output-Input Efficiency) Was the project efficiently implemented by leveraging the expertise of domestic and local partner organizations? (i.e., completion of BED of child laborers as outputs of this project)
- (Cost efficiency) Was the project completed within the planned budget?
- (Time efficiency) Was the project implemented according to the planned schedule? (ie. Accelerated learning curriculum, and accelerated teaching and learning)

Effectiveness

- (Achievement of outputs and outcomes) Were the outputs and outcomes proposed in the PDM achieved?
- (The extent to which the project ensured inclusiveness and equity for vulnerable populations) Were the project beneficiaries fairly chosen among beneficiaries from diverse backgrounds of children? Were the project's outcomes and benefits fairly distributed among beneficiaries from diverse backgrounds of children (sex, family background, parents' education level)?
- (Socio-economic/institutional impact of the project) Did the project contribute to the improvement and expansion of policies or systems related to BED/NFE or CLEP/CLCMC in the partner country (readiness)?

Impact (Preparedness)

- (Achievement of outcomes and goals) Were the outcomes and goals proposed in the PDM and TOC achieved?

Sustainability

- (Financial and institutional capacity) Does the partner country have the financial capacity (budget) to continue the project's outcomes after its completion? Are there institutional measures (laws, policies, and systems) in place to support continuation of the project's results?
- (Systems for the management of human resources) Are dedicated personnel in place to ensure the continuity of the project after its completion? Has the project contributed to building the environment where the professional capacity can be sustained and scaled up even after the project's completion?
- (Systems for the professional, community, policy, knowledge network) Has a professional, community or/and policy/knowledge network been established and maintained that can be sustained and expanded even after the completion of the project?

Additional Evaluation Criteria and Questions

Affecting Factors (Enablers and Constraints)

- What are the structural factors within the partner country and its institutions that facilitate sustainability? ((Enablers, Working factors)
- What are the structural factors within the partner country and its institutions that hinder sustainability? (Constraints)

Alignment with the partner country's development strategies and priorities

- Does the project contribute to achieving SDGs (Edu)?
- Was the project designed to reflect the development strategies and major education policy directions (including FE/NFE of the partner country)?
- Is the project aligned with Korea's ODA (Edu) and international cooperation strategies?
- Was a needs assessment conducted at the project design stage, and were the results reflected in the project?

Relevance of project design and structure

- Were the activities, outputs, and outcomes of the project appropriately designed under clear objectives?
- Were the cross-cutting issues (such as gender and human rights) considered and reflected in the project design?

Relevance of response to environmental changes and risk management

- Did the project respond appropriately to contextual changes (e.g., natural disasters, labour conflicts, market changes, civil wars, political changes) that occurred during implementation?

Internal and External Coherence

- Is the project coherent with the programs and initiatives of other ministries, agencies, and other CSOs of the Korean government?
- Is the project coherent with the programs and initiatives of other donors, institutions, and CSOs in the partner country?

B. List of In-depth Interview Questions

Part1. International and Governmental Institutions

Key Actors	Key Questions
Ministry of Labour & Employment	• What development strategies or educational policy directions does the Ministry of Labour and Employment have to improve access to basic education for child labourers? Additionally, are there any strategies or measures targeting employers in this context? • How does the Ministry of Labour and Employment collaborate with either the Ministry of Primary and Mass Education or the Ministry of Education? How are their respective roles and responsibilities divided in addressing the issue? • Was the CFK-EduCo project designed to reflect the development strategies and major education policy directions (including FE/NFE) of Bangladesh? • Is the CFK-EduCo project coherent with the programs and initiatives of Ministry of Labour & Employment? • Should there any particular cross-cutting issues (such as gender, class, income levels) considered and reflected in the project in the context of Bangladesh? • What changes are expected under the new administration regarding efforts to improve access to basic education for child labourers? • What are the key challenges and potential areas for government & policy-level sustainability in regards to the impact of the project on the implementation of child labor policies? • What kinds of project are currently being undertaken by the MOLE to improve access to basic education for child labourers? Which institutions are involved (e.g. local NGOs, international NGOs, or the Ministry of Labour and Employment itself)? If there is collaboration with NGOs, How does MOLE support NGO (e.g. financial support, human resource support, provision of space or facilities)? • What are the key challenges and potential areas for works of CLCLMC (Community-led Child Labor Monitoring Committee) and CLEP (Child Labor Elimination Platform) activities in government budgeting and potential institutionalization? • Regarding CLEP (Child Labour Elimination Platform), which is the first national platform for child labour elimination in Bangladesh: What changes has the Ministry of Labour and Employment observed since the establishment of CLEP, compared to the period before its existence? (Have there been any noticeable improvements in coordination, policy implementation, or stakeholder engagement?) • What activities are currently being carried out in collaboration with the Ministry of Labour and Employment through CLEP? • What role does the MOLE expect CLEP to play? (Are there any specific areas where the Ministry hopes CLEP can contribute more effectively (e.g. coordination, policy advocacy, capacity building, monitoring)?
District Primary Education Office	• In relation to promoting the right to basic education for child labourers living in urban slum areas, what strategies or policy directions does the Ministry of Primary and Mass Education have regarding the integration of these children into the National Primary Education (NPE) system and public schooling?

	• Are there any ongoing programs or initiatives specifically targeting child labourers who are enrolled in secondary education institutions? • Was the CFK-EduCo project designed to reflect the development strategies and major education policy directions (including FE/NFE) of Bangladesh? • Is the CFK-EduCo project coherent with the programs and initiatives of Ministry of Labour & Employment? • Should there any particular cross-cutting issues (such as gender, class, income levels) considered and reflected in the project in the context of Bangladesh? • What are the key challenges and potential areas for contribution of Bridge Schools to integration into formal education? • Are there any possibilities for support or partnership from the Ministry in areas such as school facility provision, meal subsidies, or teacher salary support? • What development strategies or educational policy directions does the District Primary Education Office have in place to improve access to basic education for child labourers? (In the case of bridge schools, the high operational costs—including building rental, meal expenses, and teacher salaries—pose a significant challenge to sustainability) • What are the key challenges and potential areas for institutionalizing the Bridge School model into the public education system, transferring students to public schools, and linking with school feeding programs?
UNICEF Office	• What are the most critical and challenged areas of education and social protection of child laborers in Bangladesh? What are newly emerging issues in the process of the post-2015 process? • How does the CFK-EduCo project contribute to achieving SDGs (Education and Child Protection)? • Should there any particular cross-cutting issues (such as gender, class, income levels) considered and reflected in the project in the context of Bangladesh? • What are the current UNICEF's initiatives for child laborers (project scale, goals, strategies, and key activities, limitation, etc.)? • Regarding CLEP (Child Labour Elimination Platform), which is the first national platform for child labour elimination in Bangladesh: What changes has the UNICEF observed since the establishment of CLEP, compared to the period before its existence? (Have there been any noticeable improvements in coordination, policy implementation, or stakeholder engagement?) • What role does the UNICEF expect CLEP to play? Are there any specific areas where the Ministry hopes CLEP can contribute more effectively (e.g. coordination, policy advocacy, capacity building, monitoring)? • What forms of collaboration are currently in place with the Ministry of Labour and Employment and the Ministry of Education to improve access to basic education for child labourers in collaboration with the UNICEF?
ILO Office	• What are the most critical and challenged areas of labour rights and social protection of child/youth laborers in Bangladesh? What are the newly emerging issues in the process of the post-2015 process for ILO?

	• How does the CFK-EduCo project contribute to achieving SDGs (Education and Child Protection)? • Should there any particular cross-cutting issues (such as gender, class, income levels) considered and reflected in the project in the context of Bangladesh? • What are the ILO's initiatives for child laborers (project scale, goals, strategies, and key activities, limitation, etc.)? • Regarding CLEP (Child Labour Elimination Platform), which is the first national platform for child labour elimination in Bangladesh: What changes has the ILO observed since the establishment of CLEP, compared to the period before its existence? (Have there been any noticeable improvements in coordination, policy implementation, or stakeholder engagement?) • What role does the ILO expect CLEP to play? Are there any specific areas where the Ministry hopes CLEP can contribute more effectively (e.g. coordination, policy advocacy, capacity building, monitoring)? • What forms of collaboration are currently in place with the Ministry of Labour and Employment and the Ministry of Education to improve access to basic education for child labourers? • The Bridge School initiative carries out activities through CLEP, CLCMC, and employers, aiming to improve access to basic education for child labourers and contribute to child labour elimination. In order to translate these efforts into more systemic outcomes—such as policy reform or institutionalization—are there any proposals or areas where further collaboration with the ILO could be pursued?
--	---

Part 2. Direct and Indirect Beneficiaries of the Project

Key Actors	Key Questions
3-6 students	• What are your favorite activities when you come to the Bridge school? • (if possible) What are the biggest differences of the Bridge School in comparison to other schools in the community? • What kind of difficulties do you have in terms of studying and continuing your studies? • What do you usually do after school hours? What kind of jobs do you do? Are there any paid works? • (if possible) What are the biggest differences of working hard and less hard chores/work that you do?
2-3 teachers	• What are the things that you are the proudest of the Bridge school? • (if possible) What are the biggest differences of the Bridge School in comparison to other schools in the community? • (Assessing sustainability) What are the things you do that are the proudest while you are teaching at the Bridge school? • (if possible) What are the biggest differences of working at the Bridge School in comparison to other schools in your community? • (Reviewing project performance) What are the most difficult issues in regards to learning outcomes, improvement in access to education for the

	children in the community? • What kind of difficulties do you have in terms of continuing your job? • What do you usually do after school hours? What kind of jobs do you do? Are there any paid works? • (if possible) additional questions in regards to teachers' employment conditions and support for capacity building
2-3 parents	• What are the things that you are proudest of sending your children to Bridge school? • (if possible) What are the biggest differences between the Bridge School and other schools in the community? • (if possible) What are the biggest differences of working at the Bridge School in comparison to other schools in your community? • (Reviewing project performance) What kind of difficulties do you have in terms of continuing your children's education?
Employers	• Please introduce when and how you came to know the Bridge School and the school project team. • (Before and After) Before you knew about the Bridge School Project, what did you think about the working children? How has it changed? • (Before and After) Before you knew about the Bridge School Project, what did you think about the fact that children's schooling? How has it changed? • What are the key challenges and limitations for employers (small businesses) in order not to hire children for your type of work? • What are the potentials for employers (small businesses) to avoid hiring children for the future?
Community or Platform-Based Activities (CLCLMC)	• Please introduce the three most important CLCLMC activities between 2024 and 2025. • What are the most notable achievements of reducing child labor through monitoring and responses? • What are the things that you feel most rewarded by participating in the CLCLMC activities? • What are the potentials and limitations for continuing the CLCLMC activities after project completion?
Community or Platform-Based Activities (CLEP)	• Please introduce the three most important CLEP activities between 2024 and 2025. • What are the most notable achievements of coordination and policy-strategic dialogue and on child labor issues? • What are the things that you feel most rewarded, participating the CLEP activities? • What are the potentials and limitations for continuing the CLCLMC activities after project completion? • Are there any opportunities and potentials to connect future projects with multi-donor funds and government financing through CLEP?

Part 3. Other Partners

Key Actors	Key Questions
BRAC Office	• What are the most critical and challenged areas of labour rights and social protection of child/youth laborers in Bangladesh? What are the newly emerging issues in the process of the post-2015 process for BRAC? • What are the BRAC's initiatives for child laborers (project scale, goals, strategies, key activities, limitations, etc.) • Are there any support or partnership from the Ministry in areas such as school facility provision, meal subsidies, or teacher salary support for BRAC project? • Are there any ongoing programs or initiatives specifically targeting child labourers who are enrolled in secondary education institutions? • Should any particular cross-cutting issues (such as gender, class, income levels) be considered and reflected in the project in the context of Bangladesh? • What changes has the BRAC observed since the establishment of CLEP, compared to the period before its existence? (Have there been any noticeable improvements in coordination, policy implementation, or stakeholder engagement?) • What role does the BRAC expect CLEP to play? (Are there any specific areas that CLEP can contribute more effectively (e.g., coordination, policy advocacy, capacity building, monitoring)?)
Academia (University Specialist)	• What are the most critical and challenged areas of labour rights and social protection of child/youth laborers in Bangladesh? • What are newly emerging issues in the process of the post-2015 process for child/youth laborers in Bangladesh? • What are the research and evaluation gaps (understudied areas) for child laborers (data availability, scale, and key research strategies activities, limitation, etc.)?

C. Field Evaluation Process and Activities

Field Evaluation Activities (Period: October 18 – October 24)

Week	Key Activities
Saturday	(AM) First Workshop (RBM/M&E) (PM) interviews with key beneficiaries/partners
Sunday	(AM) visit to schools (PM) interviews with key beneficiaries/partners(esp. Business owners)
Monday	(AM) Visit to KOICA, Interview at KOICA (PM) UNICEF, BRAC,
Tuesday	(AM) visit to schools (PM) interviews with key beneficiaries/partners
Wednesday	(AM) Interviews with the Ministry of Labour and Employment (PM) Interviews with the Ministry of Education (PM) Bureau of Non-Formal Education (IF POSSIBLE)
	Workshops and Debriefing Meetings
Thursday	Departure from Dhaka, Bangladesh

Field Evaluation Photos



D. End-line Survey Information⁷

End-line survey team's report (2025) presents an overview of the respondents, research sites, and key respondents received. It includes information on respondents by sex, age, enrollment status, and they received through the project. In addition to the overall demographic profile, detailed respondent criteria as below. The key findings of the End-line evaluation in relation to the project indicators are first shown below:

■ Key findings overview

Indicators	Endline Data	Target	Change	Remarks
Impact				
% of 8 bridge school students enrolled in lower secondary school	N/A	40%	-	As the academic year has not yet been completed, it was not possible to accurately determine the actual enrollment status.
Outcome				
1.1: % of bridge schools approved by government as non-formal educational facilities	100%	100%	--	Target achieved
1.2: % of bridge school students who completed primary education course	N/A	70%	-	Since this indicator will be assessed later, we added the number of graduation exam participants as a substitute indicator.
2.1: % of child labourers with improved awareness of educational rights (male/female)	Survey Data: Aware: 40.6% Boys: 41.5% Girls: 39.7%	40%	25.62% (↑)	Target achieved; awareness measured as ability to identify at least 3 aspects of educational rights.
2.2: % of duty bearers with improved awareness of educational rights (male/female)	Survey Data: Aware: 60.8% Male: 60.8% Female: 60.7%	40%	40.54% (↑)	Exceeded target; strong recognition of children's right to education and related benefits.
Output				
1.1.1: of bridge schools equipped with infrastructure	8	8	--	Target achieved
1.2.1: # of children enrolled in bridge education program	Documents Review: Total: 800 Male: 400 Female: 400	Total: 800 Male: 400 Female: 400		Target achieved
1.2.2: # of children received psycho-social counseling	Survey Data: Receiving Psycho-Social Counseling • Received counseling – 97.8% • Always attend –	Total: 240 Male: 120 Female: 120	--	During the KII, teachers mentioned that many children are growing up in challenging environments, which has made them more aggressive and different in

⁷ End-line Assessment is conducted by the Centre for Research and Development (CRD)

Indicators	Endline Data	Target	Change	Remarks
	48% • Often attend – 31.7% • Occasionally attend – 13.7% • Rarely attend – 3.3% • Did not receive counseling – 2.2% Document Review: Total: 1996 Male: 973 Female: 1023			their behavior. To help reduce this aggression, most of these children have been provided with psycho-social counseling.
1.2.3: # of slow learners receiving extra coaching	Survey Data: Extra Coaching Classes • Attend extra coaching – 84.5% • Do not attend – 15.5% Document Review: Total: 2,181 Students (Male: 1094 students & Female: 1087 students) Year – 1: 581 students (Male: 304 & Female: 277) Year – 2: 800 students (Male: 395 & Female: 405) Year – 3: 800 students (Male: 395 & Female: 405)	Total: 1200 Male: 600 Female: 600	-	Teachers during the KII discussions reported that a significant number of students struggle academically, as they depend only on classroom learning. To address this learning gap, more students have been engaged in extra coaching classes.
1.2.4: # of students who received school materials and meals	Survey Data: School Materials Received • Students receiving school materials – 99.6% • Did not receive – 0.4% Meals Received • Students receiving meals daily – 99.6% • Receives 3–4 times a week – 0.4% Document Review: Total: 2400 students	Total: 2400 Male: 1200 Female: 1200	-	Target achieved


Indicators	Endline Data	Target	Change	Remarks
	(Male: 1190 & Female: 1210) Year – 1: 800 students (Male: 400 & Female: 400) Year – 2: 800 students (Male: 395 & Female: 405) Year – 3: 800 students (Male: 395 & Female: 405)			
1.2.5 # of 8 bridge school students who have completed the primary education course (who passed the exam for next grade) / 2 nd year (Grade 3), 3 ^{year} (Grade 4,5/per 6months	Documents Review: Total: 1600 students (Male: 790 students & female: 810 students) Year – 2: 800 students (Male: 395 & Female: 405) Year – 3: 800 students (Male: 395 & Female: 405)	Total: 1280 Male: 640 Female: 640	-	Academic year not yet completed; all surveyed students expressed willingness to complete primary education by end 2025
1.3.1: # of 3-year condensed curriculum developed	1	1	-	Target achieved
1.3.2: # of teachers trained on bridge education program	Documents Review: Total: 72 Year – 1: 24 Year – 2: 24 Year – 3: 24	96	-	Ongoing activities
2.1.1: # of campaigns and anniversary events to advocate child labourer's right to education	Documents Review: Total: 10 times Year - 1: 4 times Year – 2: 4 times Year – 3: 2 times	12	-	Ongoing activities
2.1.2: # of employers and local residents who participated in sessions to improve the awareness of educational rights of child labourers	Documents Review: Total: 2,965 (Male: 1,121 & Female: 1300) • Year 1: 1,658 (Male: 590 & Female: 1,068) • Year 2: 763 (Male: 531 & Female: 232) • Year 3: 544	2160	-	Over achievement KII information reveals that they were able to convince community members and employers to attend the meetings, which further enhanced their knowledge. This effort also contributed to raising overall community awareness. Additionally, community members and employers have been encouraging others to become aware as well

Indicators	Endline Data	Target	Change	Remarks
2.1.3: # of bridge school students who participated in sessions to improve awareness of children's rights and educational rights	Survey Data Participation in Awareness Sessions • Participated – 94.1% • Never participated – 5.9% Documents Review: Total: 2211 students Year – 1: 800 students Year – 2: 808 students Year – 3: 603 Students	Total: 2400 Male: 1200 Female: 1200	-	Ongoing activities
2.1.4: # of parents who participated in sessions to improve awareness of children's rights and educational rights	Survey Data Parents' Participation in Awareness Sessions • Participated – 86.4% • Never participated – 13.6% Documents Review: Total: 2603 people (Male: 858 & Female: 1,745) • Year 1: 866 people (Male: 156 & Female: 730) • Year 2: 1,107 people (Male: 402 & Female: 705) • Year 3: 610 people (Male: 300 & Female: 310)	Total: 2400 Male: 1200 Female: 1200	-	During our KII, we discussed with teacher's regarding the low participation of male parents in awareness sessions. They mentioned that most male members are usually busy during the daytime, when these meetings are generally scheduled.
2.2.1: # of people who participated in CLCLMC	Documents Review: Total: 264 people Year – 1: 88 people Year – 2: 88 people Year – 3: 88 people	Total: 264	-	Target achieved
2.2.2: # of monitoring visits at workplace and household	Documents Review: 88	96	-	This is an ongoing activity!

Indicators	Endline Data	Target	Change	Remarks
2.2.3: # of CLCLMC members participated in sharing meetings	Documents Review: Total: 132 Year – 1: 24 Year – 2: 108	48	-	This activity is still ongoing. Although the target was to arrange meetings with 16 members, by the end of the year CLCLMC members and SMC members from all schools were included.
2.3.1: # of participants in the joint workshop to ensure the educational rights of child labourers	Documents Review: Total: 325 people Year – 2: 147 people Year – 3: 178 people	120	--	Activity is still ongoing.
2.3.2: # of policy proposal to provide educational services for child labourers	0	1		This activity is still ongoing

■ Information on the Survey

Out of a total of 622 respondents, survey data was collected from 536 respondents, while qualitative data was collected from 86 participants. Among the 536 survey respondents, 265 were parents and 271 were students. Regarding gender distribution, among the students group included 136 girls and 135 boys, while the parents group consisted with 135 were females and 130 males. In addition, among the 86 qualitative participants, 46 were female and 40 were male.

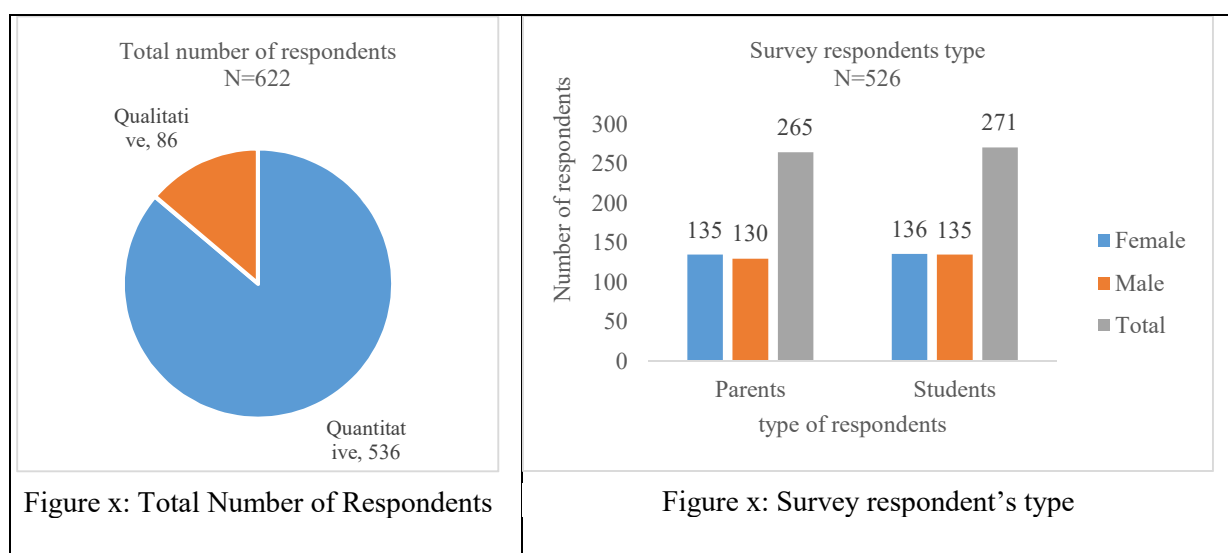

Parents' Age Range: In this survey, most parents were between 21 and 50 years old, representing the largest share of the sample, with the 31-40 years age group showing the highest proportion in both genders. Overall, 46.4 percent of parents were aged 31-40 years, followed by 24.9 percent in the 41-50 years group and 16.6 percent in the 21-30 years group. A smaller proportion was above 50 years (10.2 percent), and only 1.9 percent were aged 18-20 years. Among female parents, 51.9 percent were in the 31-40 years bracket, followed by 28.1 percent in the 21-30 years group, while only 3.0 percent were above 50 years. In contrast, male parents were more evenly distributed, with 40.8 percent aged 31-40 years, 33.8 percent in the 41-50 years group, and 17.7 percent above 50 years. These results indicate that survey participants were primarily

adults, with female parents skewed toward younger ages and male parents more represented in older age categories (details are in annex).

Children's Age Range: Most children in the survey were aged 12–13 years, accounting for 63.5 percent of the sample. This was followed by those aged 14–15 years, representing 18.5 percent, and 10–11 years, comprising 16.2 percent of respondents. A very small proportion of children aged 16–17 years, all of whom were boys, and no children under 10 years were included in the sample. (details are in annex)

A total of 271 students participated in the survey, with 136 females and 135 males. These students were enrolled across eight Bridge Schools. Each school had a nearly equal number of students, ranging from 32 to 35 participants from each school. The distribution of boy and girls students was almost equal across all schools.

- **Monthly Household Income:** The data show that respondents' household earnings are concentrated in specific ranges. Most households earn between BDT 20,000 and 29,999 per month, with 22.6% earning BDT 20,000–24,999 and 30.6% earning BDT 25,000–29,999, making these the most common income levels among the surveyed population. Earnings below BDT 15,000 are relatively rare (1.5%), and only a small fraction of households earn above BDT 40,000 (2.3%).
- **Monthly Household Expenditure:** Expenditure patterns broadly reflect income distribution, although some differences are evident. About 24.5% of respondents spend BDT 15,000–19,999, while 31.3% spend BDT 20,000–24,999, indicating that some lower-income households may spend close to or slightly above their earnings. In higher expenditure ranges, fewer respondents are observed: BDT 30,000–34,999 (10.2%), BDT 35,000–40,000 (7.5%), and above BDT 40,000 (1.9%), suggesting that higher earners may spend proportionally less relative to their income. Overall, both income and expenditure are heavily concentrated in the BDT 20,000–29,999 range, reflecting the predominant earning and spending patterns of the surveyed households. When compared with BBS HIES 2022, the average monthly household income and expenditure in urban areas were approximately BDT 45,757 and BDT 41,424 (HIES, 2022). This indicates that the surveyed slum households generally earn and spend below the urban average, highlighting their relatively constrained economic situation. Extreme low and high income or expenditure ranges represent a small portion of respondents, emphasizing the concentration of households within the mid-income range of the slum population.

Table10: Respondents monthly income range

Response	Monthly Income (% of Respondents)	Monthly Expenditure (% of Respondents)
<15000	1.5	5.7
15000-19999	13.2	24.5
20000-24999	22.6	31.3
25000-29999	30.6	18.9
30000-34999	18.1	10.2
35000-40000	11.7	7.5
>40000	2.3	1.9
Total	100.0	100.0

- **Children's Monthly Income:** The distribution of children's monthly income shows that earnings are generally lower than household income. Most children earn between 1501–3000 BDT per month, with

21.5% earning 1501–2000 BDT, 19.8% earning 2501–3000 BDT, and 24.3% earning above 3000 BDT, while a large proportion of girls earn in the lower ranges (1001–2000 BDT) and boys are more concentrated in the higher ranges (2501+ BDT), highlighting a clear gender disparity. In comparison, household income in the same population is predominantly in the BDT 20,000–29,999 range, and monthly household expenditures largely reflect this income, with the same 20,000–29,999 range being the most common. This indicates that children’s earnings constitute only a small fraction of total household income, and households rely primarily on adult earners. While some older children may contribute substantially to the household income, their individual earnings are generally insufficient to match the household-level expenditures, which are necessary to meet family needs in urban slums. Overall, the comparison shows that children’s income complements but does not replace household income, and expenditures are supported mainly by the larger household income, with children’s contributions forming a minor yet important supplement, particularly in higher-earning boys.

Table 11: Children income range

Response	Girls	Boys	Total (n2'=177)
<500	3.4	0.0	1.7
500-1000	14.9	6.7	10.7
1001-1500	23.0	4.4	13.6
1501-2000	29.9	13.3	21.5
2001-2500	4.6	12.2	8.5
2501-3000	10.3	28.9	19.8
>3001	13.8	34.4	24.3
Total	100.0	100.0	100.0

Table 12: Age range for parents

Age range	Female	Male	Total
18-20	0.7	3.1	1.9
21-30	28.1	4.6	16.6
31-40	51.9	40.8	46.4
41-50	16.3	33.8	24.9
>50	3.0	17.7	10.2
Total	100.0	100.0	100.0

Table 13: Age range for children

Age range	Girls	Boys	Total
<10	0.0	0.0	0.0
10-11	18.4	14.1	16.2
12-13	67.6	59.3	63.5
14-15	14.0	23.0	18.5
16-17	0.0	3.7	1.8
Total	136	135	271

Table 14: Household level income and expenditure

Income range	Income	Expenditure
<15000	1.5	5.7
15000-19999	13.2	24.5

20000-24999	22.6	31.3
25000-29999	30.6	18.9
30000-34999	18.1	10.2
35000-40000	11.7	7.5
>40000	2.3	1.9
Total	100.0	100.0

Table 15: Income of children engaged with work

Response	Girls	Boys	Total (n2'=177)
<500	3.4	0.0	1.7
500-1000	14.9	6.7	10.7
1001-1500	23.0	4.4	13.6
1501-2000	29.9	13.3	21.5
2001-2500	4.6	12.2	8.5
2501-3000	10.3	28.9	19.8
>3001	13.8	34.4	24.3
Total	100.0	100.0	100.0

Table 3: Awareness of children's right to education (by students)

Response	Girls	Boys	Total (n2=271)
Yes	83.8	78.5	81.2
No	4.4	8.9	6.6
Heard this term but do not know about it	11.8	12.6	12.2
Total	100.0	100.0	100.0

Table 17: Perception about children's right to education (by students)

Response	Girls	Boys	Total (n2=271)
All children should have access to education	79.4	77.0	78.2
Education should be free	47.8	31.9	39.9
Any child can go to any school	38.2	28.1	33.2
All children should receive similar types of education	27.2	37.0	32.1
Parents should send their children to school	33.1	17.8	25.5
Education materials should be made available for all children	19.9	20.7	20.3
GoB should ensure education for all children	19.1	20.7	19.9

Table 18 : Perception about the accessibility of working children's right to education (by students)

Response	Girls	Boys	Total (n2=271)
To a great extent	86.8	65.2	76.0
To some extent	13.2	31.9	22.5
To a poor extent	0.0	3.0	1.5
Not at all	0.0	0.0	0.0
Not sure	0.0	0.0	0.0
Total	100.0	100.0	100.0

Table 19: Perception about children's right to education (by parents)

Response	Female	Male	Total (n1=265)
All children should have access to education	88.9	86.9	87.9
Education should be free	60.0	36.9	48.7
Parents should send their children to school	46.7	50.0	48.3
All children should receive similar types of education	36.3	46.2	41.1
Any child can go to any school	42.2	29.2	35.8
School authority is bound to admit children	25.9	29.2	27.5
GoB should ensure education for all children	31.1	22.3	26.8
All types of children should be treated equally in school	19.3	30.8	24.9
Education materials should be made available for all children	28.1	16.2	22.3

Table 4: Respondents' views on essential of education

Response	Female	Male	Total (n1=265)
Education reduces poverty	95.6	79.2	87.5
Education can prevent child labour	78.5	56.9	67.9
Education empowers children to reach their full potential	28.1	68.5	47.9
Education decreases social inequality	40.7	38.5	39.6
Don't know	0.7	0.8	0.8

Table 5: Respondents' participation in awareness sessions (by students)

Response	Girls	Boys	Total (n2=271)
Yes	132	123	255
No	4	12	16
Total	136	135	271

Table 6: Children's participation frequency in awareness sessions

Response	Girls	Boys	Total
Always	90	36	126
Often	35	52	87
Occasionally	6	28	34
Rarely	1	7	8
Never			
Total	132	123	255

Table 23: Sessions' impact on awareness of rights and child labour (by students)

Response	Girls	Boys	Total
To a great extent	114	62	176
To some extent	18	61	79
To a poor extent	1	5	6
Not at all	0	0	0
Not sure	3	7	10
Total	136	135	271

Table 24: Respondents' participation in awareness sessions (by parents)

Response	Female	Male	Total
Yes	131	98	229
No	4	32	36
Total	135	130	265

Table 75. Parent's participation frequency in awareness sessions

Response	Female	Male	Total
Always	51	24	75
Often	48	33	81
Occasionally	28	26	54
Rarely	4	15	19
Never	0	0	0
Total	131	98	229

Table 8: Effectiveness of awareness campaign (by parents)

Response	Female	Male	Total
Very effective	78	38	116
Effective	51	53	104
Somewhat effective	2	6	8
Not effective	0	1	1
Total	131	98	229

Table 27. Number of children enrolled in bridge school education program (Parents)

From whom did you first learn about the Bridge School?			
Response	Female	Male	Total
NGO staff/community worker	2	1	3
Neighbors/ Relatives	65	73	138
Teacher	60	49	109
CLCLMC Members	5	5	10
From other students	2	2	4
Banner of this school	1		1
Total	135	130	265
How many children of yours are currently studying at bridge school?			
Response	Female	Male	Total
1	124	116	240
2	11	13	24
3		1	1
Total	135	130	265
What were the main reasons for admitting your children to the bridge school?			
Response	Female	Male	Total
We now understand the necessity of education	96	85	181

To make his/ her future bright	90	63	153
NGO provides better facilities	131	111	242
To keep him/ her away from crime	55	50	105
Better environment for study		3	3
Financial unstability	2	2	4
Location is near to home	1	1	2
Opportunity to study with work		3	3
There is no government school nearby	1		1
Total	135	130	265

Table 9 Number of children received psycho-social counseling (Students)

Do you know about the counseling session?			
Response	Girls	Boys	Total
Yes	132	128	260
No	4	7	11
Total	136	135	271
Have you received counseling to help you feel better, express your emotions, or solve problems?			
Response	Girls	Boys	Total
Yes	133	129	262
No	3	6	9
Total	136	135	271
How often do you attend counseling sessions?			
Response	Girls	Boys	Total
Always	86	44	130
Often	35	51	86
Occasionally	10	27	37
Rarely	2	7	9
Never	3	6	9
Total	136	135	271
To what extent are the counseling sessions helpful in dealing with challenges?			
Response	Girls	Boys	Total
To a great extent	113	69	182
To some extent	18	55	73
To a poor extent		5	5
Not at all		1	1
Not sure	5	5	10
Total	136	135	271

Table 29 Number of slow learners received extra care by the teachers (Students)

Do you experience any difficulties understanding the lesson in school?			
Response	Girls	Boys	Total
Yes	54	49	103
No	82	86	168

Total	136	135	271
Do you ever attend the extra coaching class?			
Response	Girls	Boys	Total
Yes	115	114	229
No	21	21	42
Total	136	135	271
Why don't you participate in the extra coaching classes?			
Response	Girls	Boys	Total
I don't have time because of work	6	11	17
I am not interested	13	12	25
I don't understand the lessons			
Lack of teacher's interest in coaching class			
Do not feel the necessity	5		5
Total	21	21	42
How many hours per week do you attend the extra coaching sessions?			
Response	Girls	Boys	Total
Less than 2 hours	90	81	171
2–4 hours	18	31	49
5–7 hours	7	2	9
Total	115	114	229
To what extent has the extra coaching improved your understanding of the lessons?			
Response	Girls	Boys	Total
To a great extent	87	55	142
To some extent	28	53	81
To a poor extent		5	5
Not at all		1	1
Not sure			
Total	115	114	229

Table 30. Number of students who received school materials and meal (Students)

Do you receive any materials from the bridge school?			
Response	Girls	Boys	Total
Yes	136	134	270
No		1	1
Total	136	135	271
Which of the following materials do you receive?			
Response	Girls	Boys	Total
Textbook	135	134	269
Uniform	135	134	269
Writing materials (paper, pencil, pen etc.)	136	134	270
Bag	134	133	267
Umbrella	4		4
Total	136	134	270
How often do you receive meals at school? (on weekly basis)			
Response	Girls	Boys	Total

Daily	136	134	270
3 - 4 times a week		1	1
Rarely			
Total	136	135	271
To what extent were the school materials and meals useful in supporting your learning?			
Response	Girls	Boys	Total
To a great extent	131	103	234
To some extent	5	30	35
To a poor extent		1	1
Not at all			
Not sure		1	1
Total	136	135	271
